



P3.express

The minimalist project management system

**An overview of
the system**

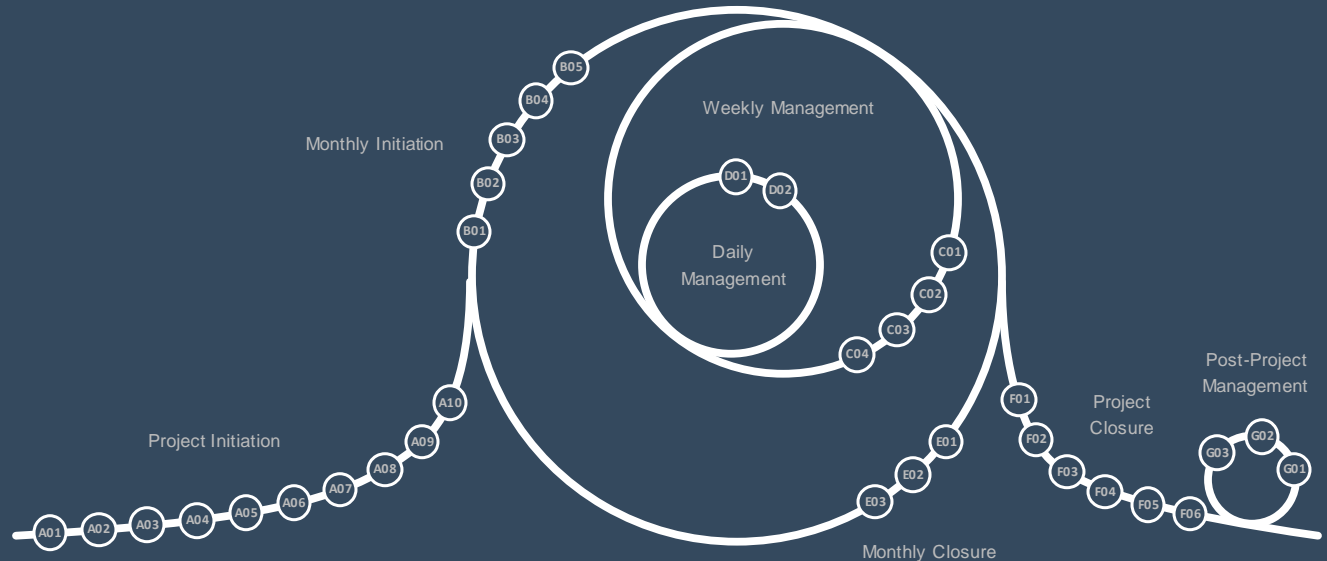


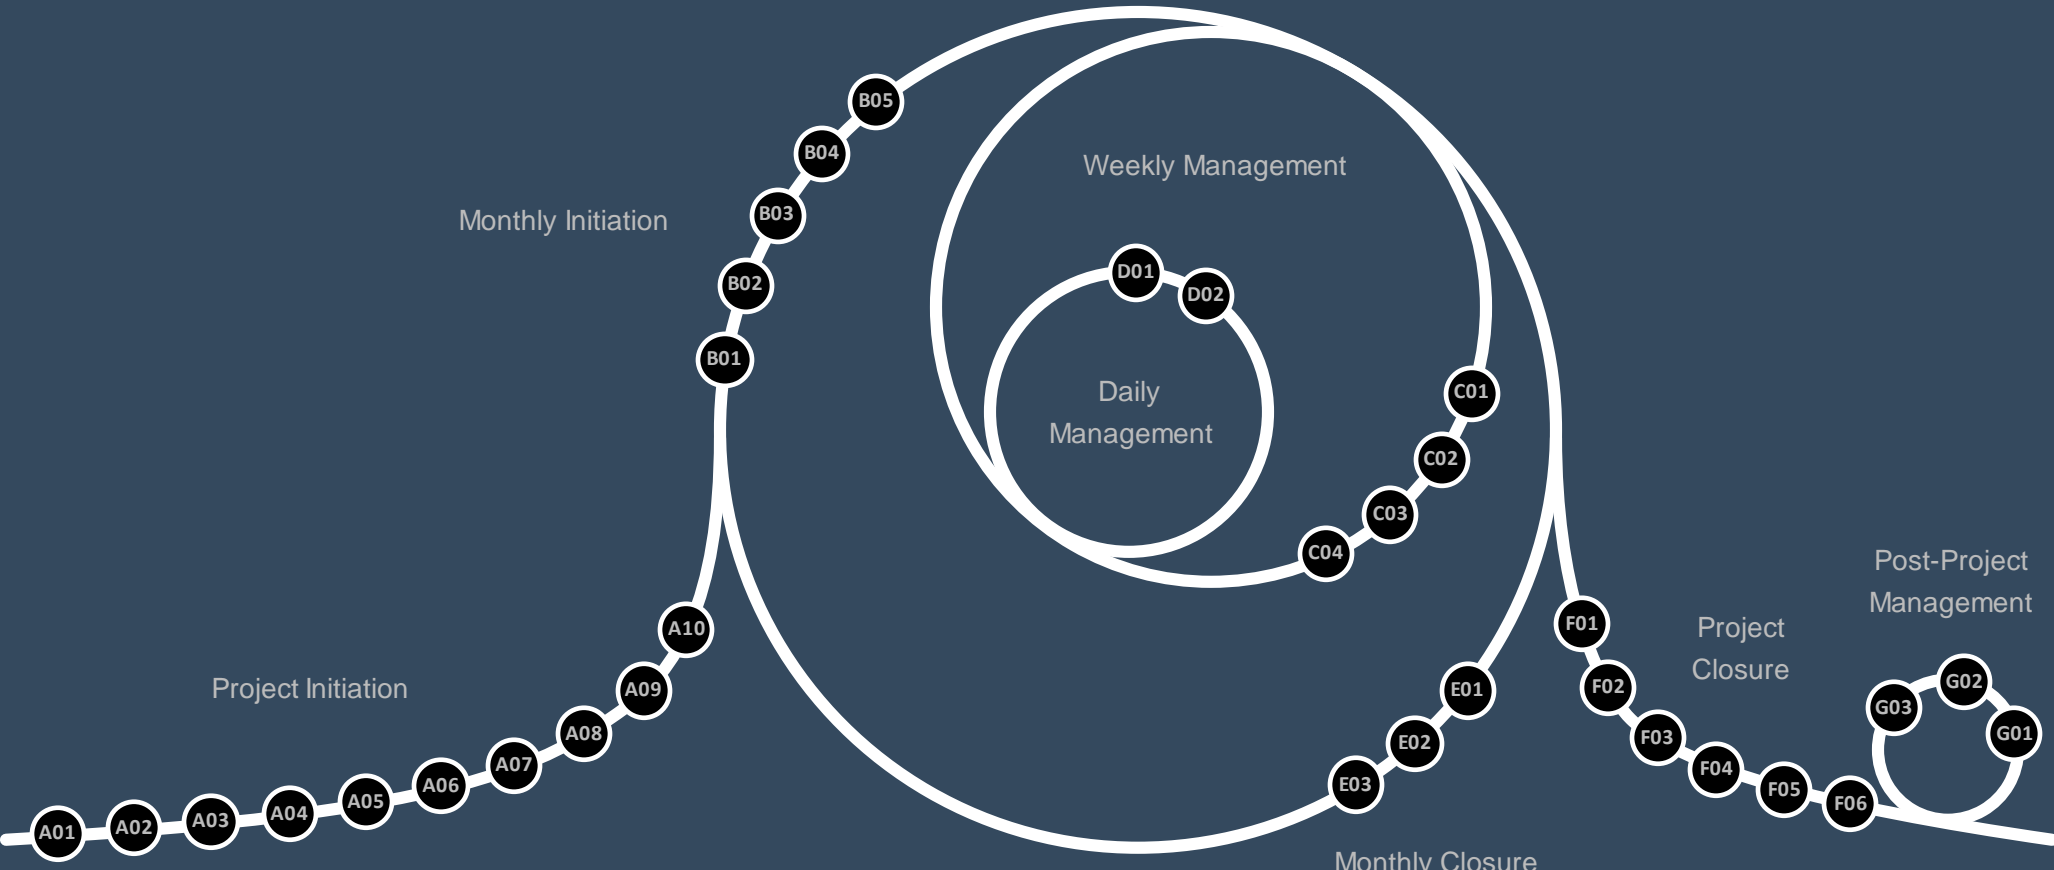




A

Project Initiation

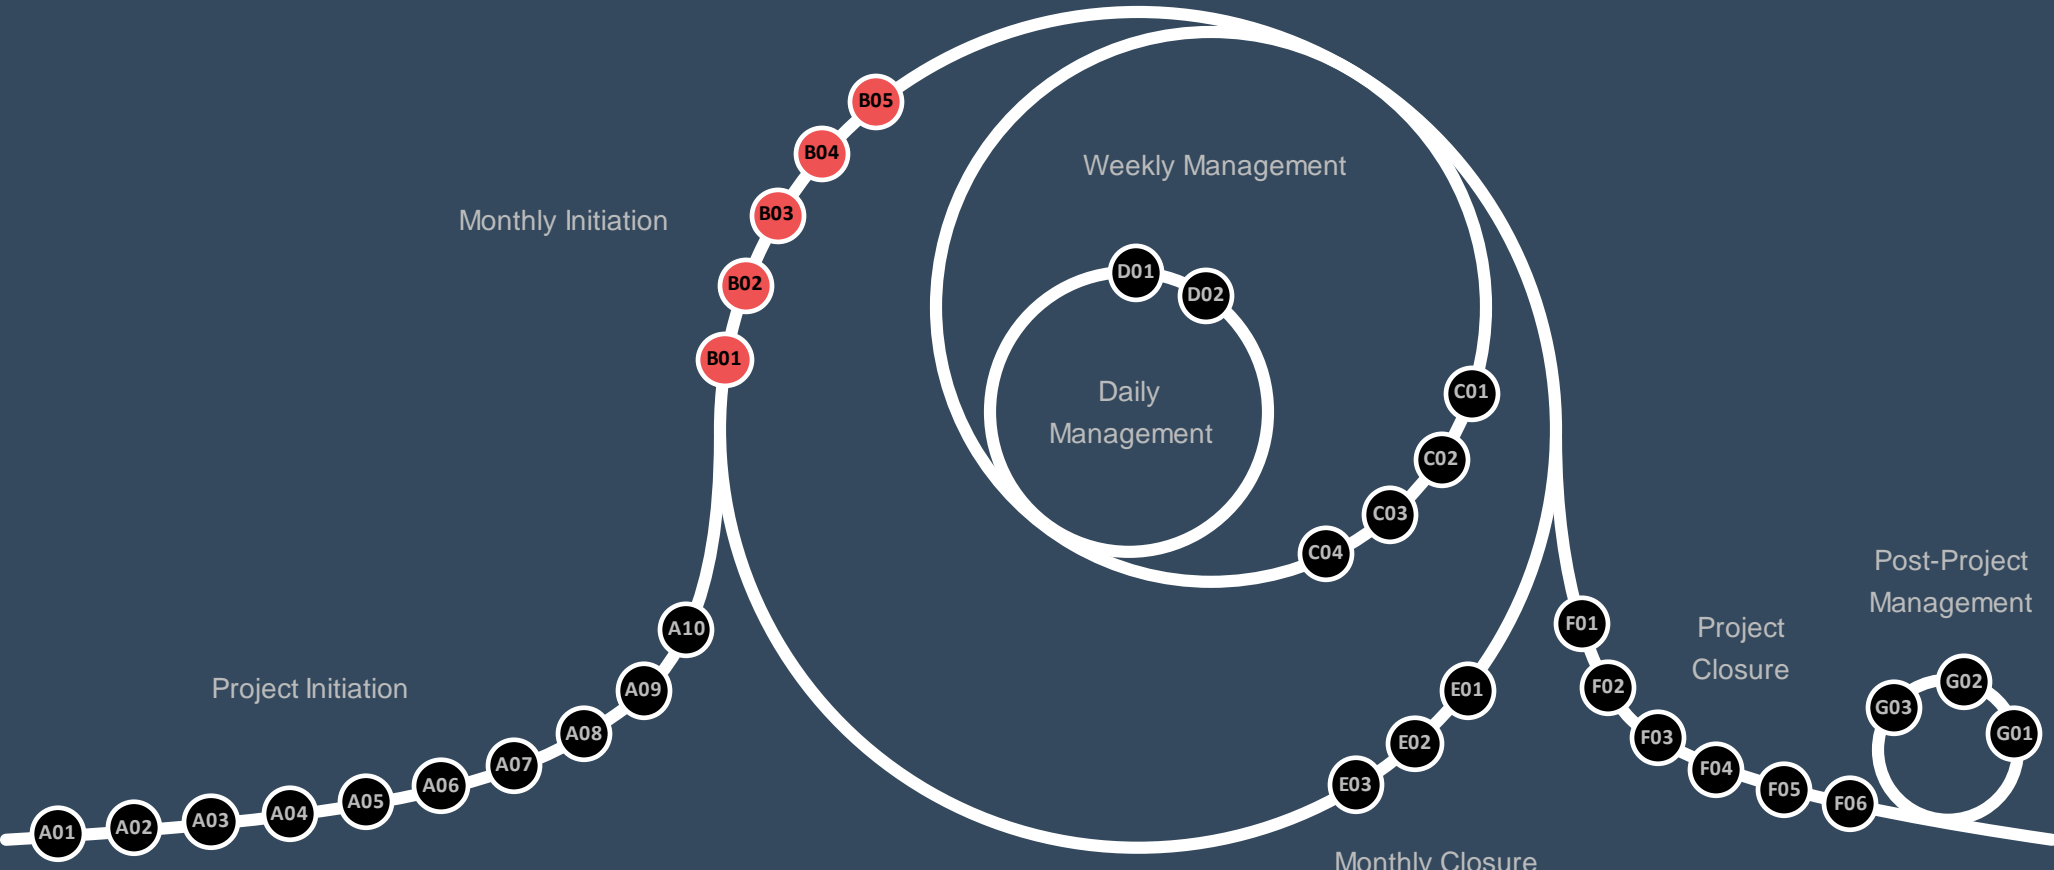

B


Monthly Initiation

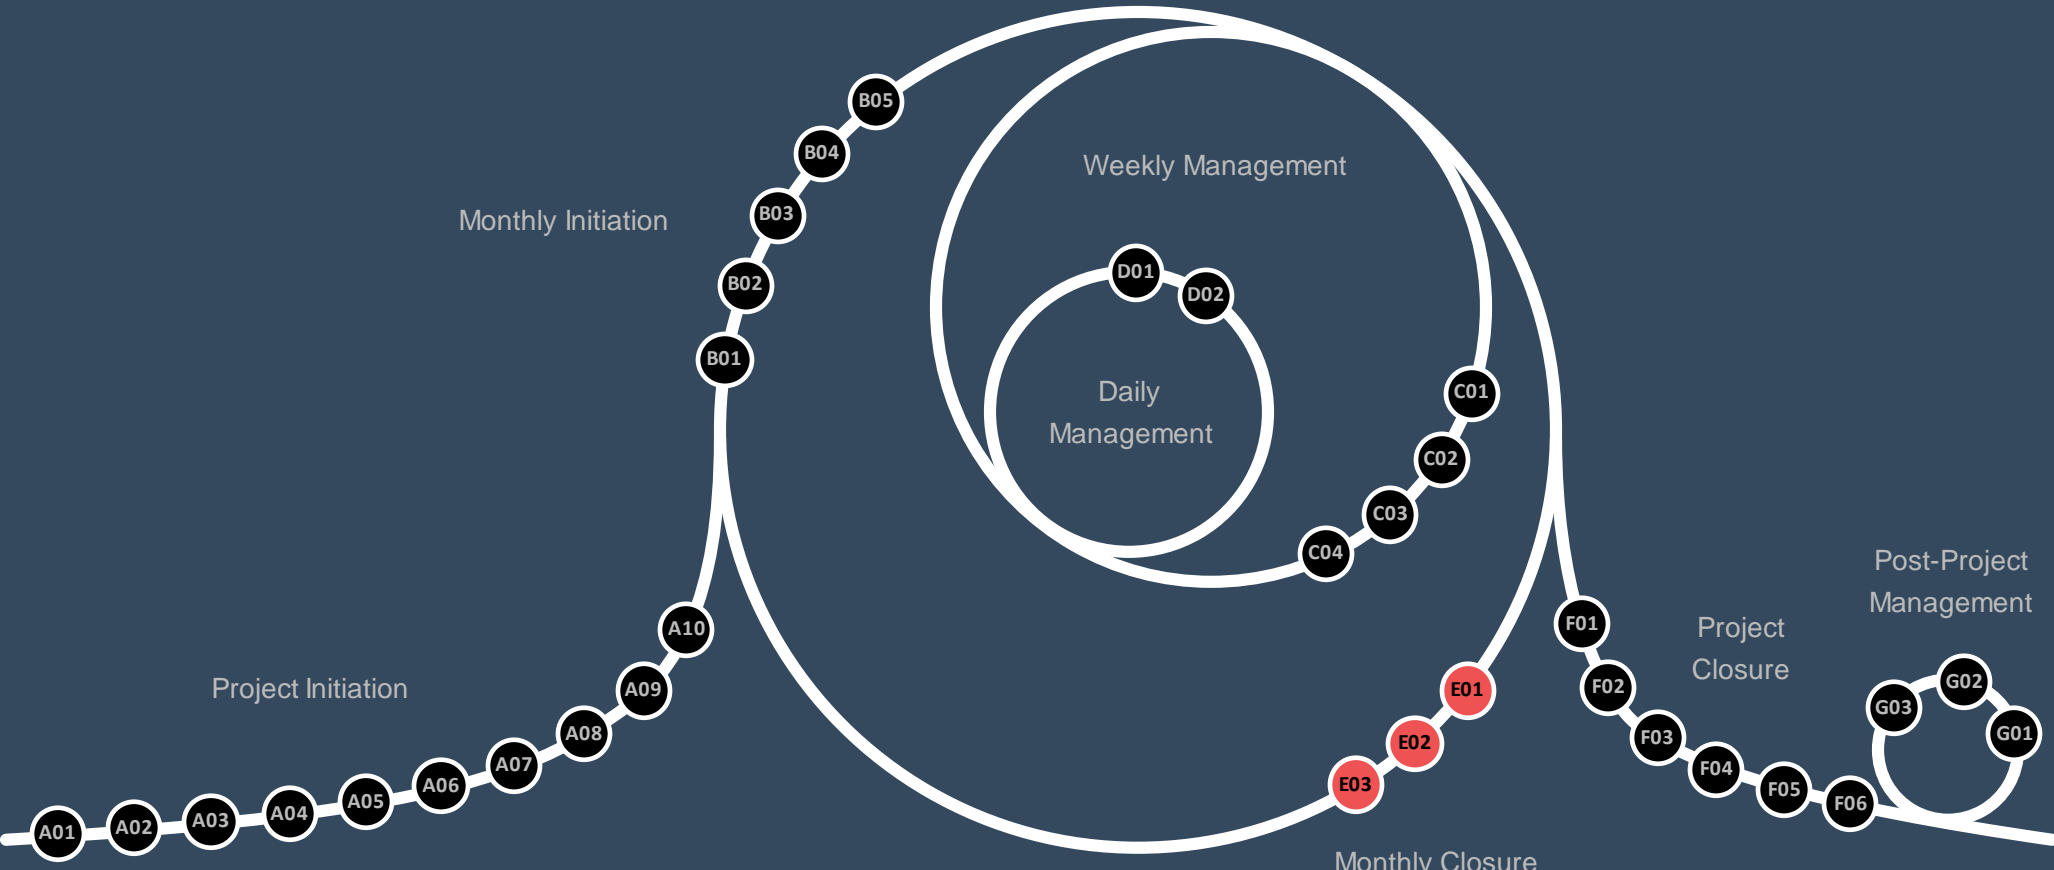

E


Monthly Closure




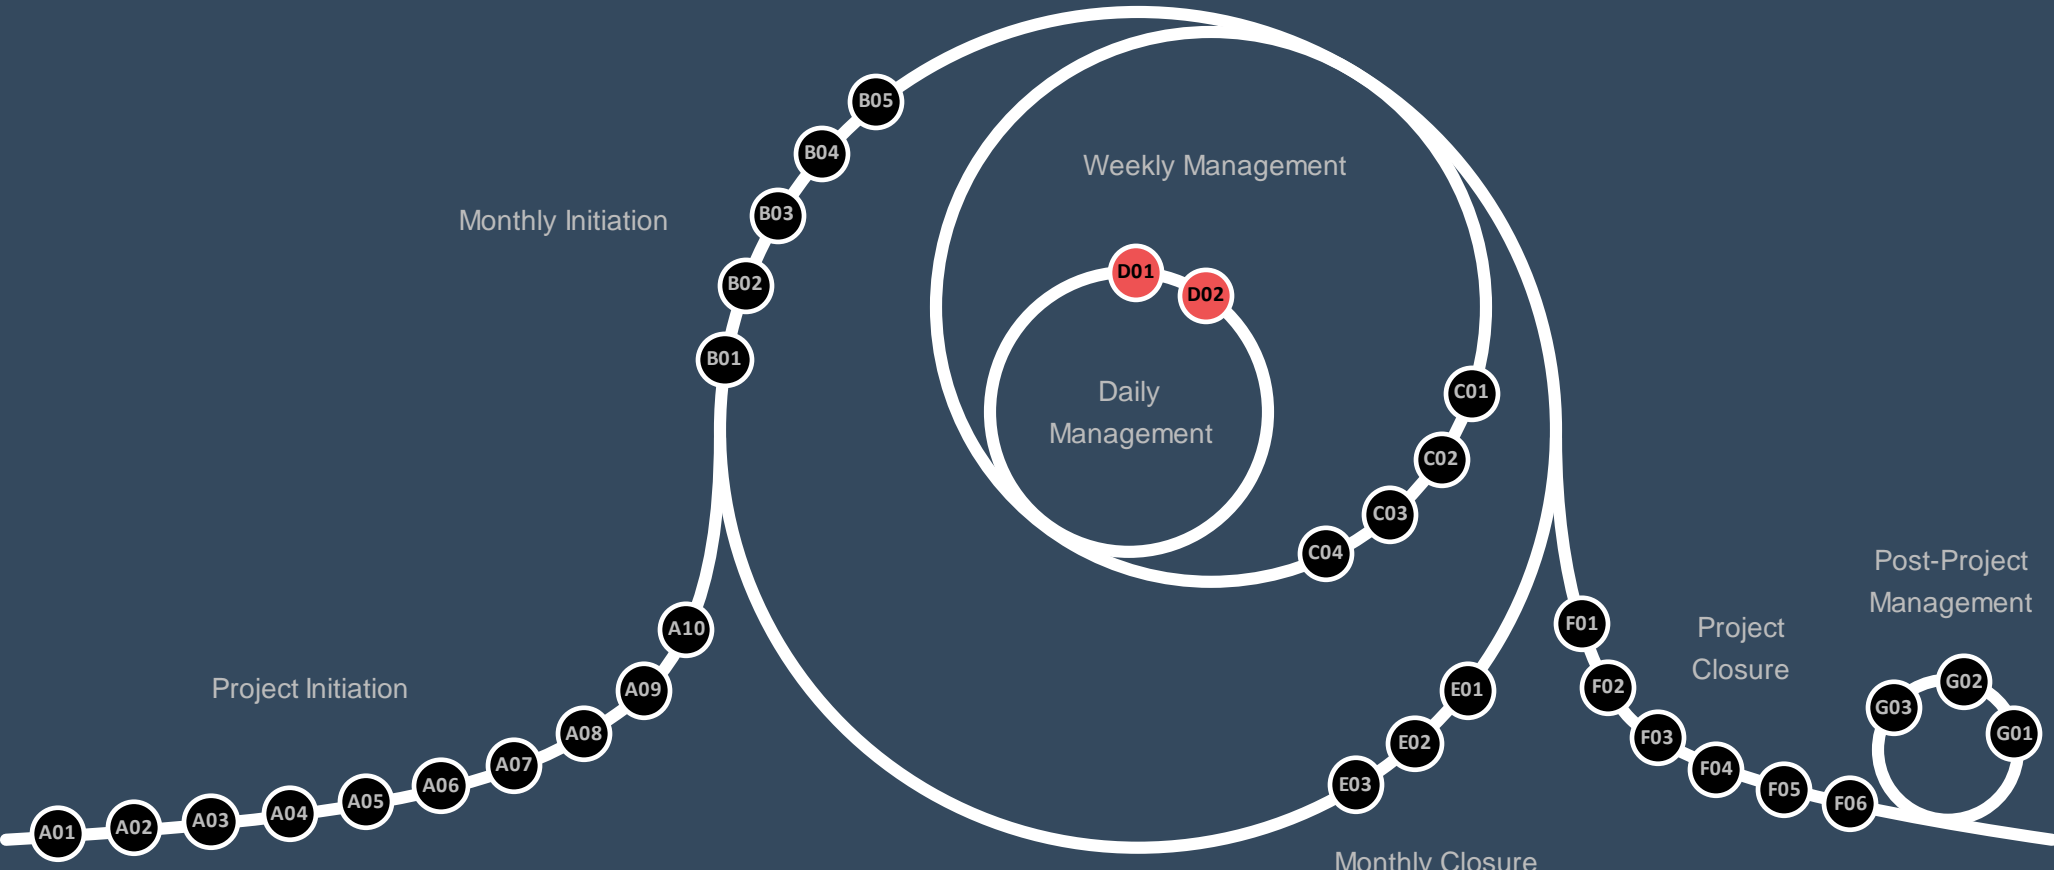


D

Daily Management

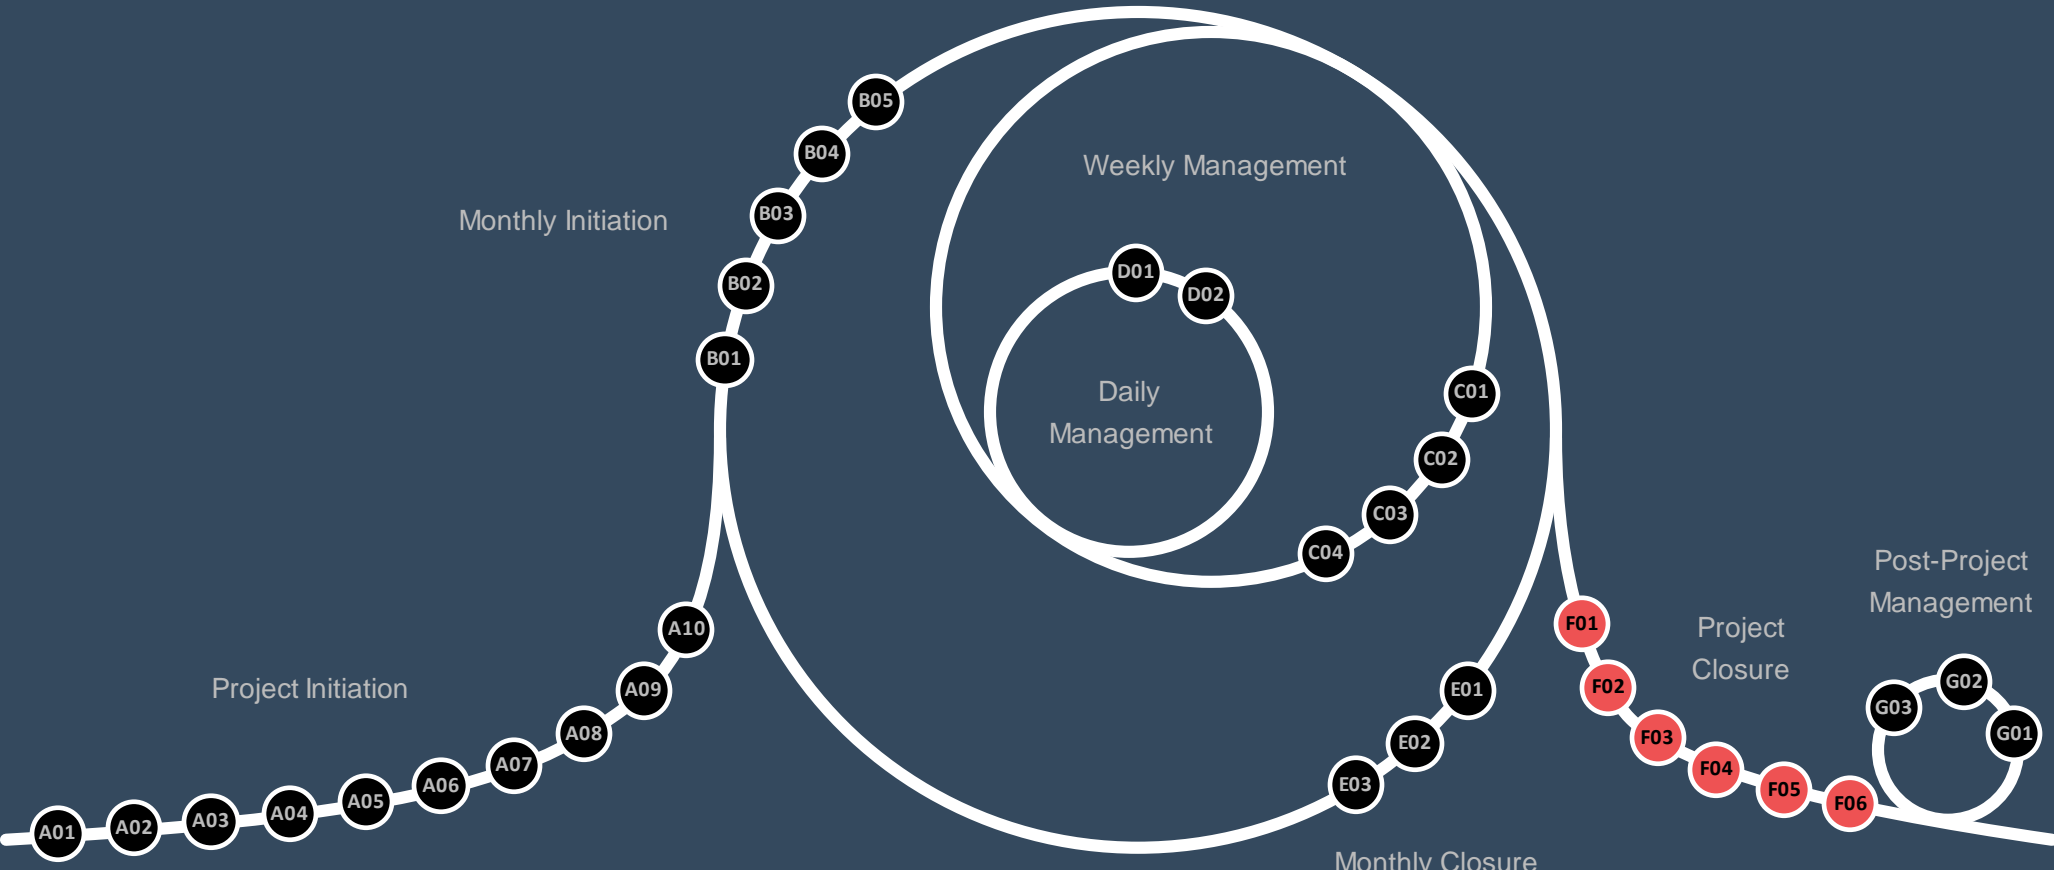


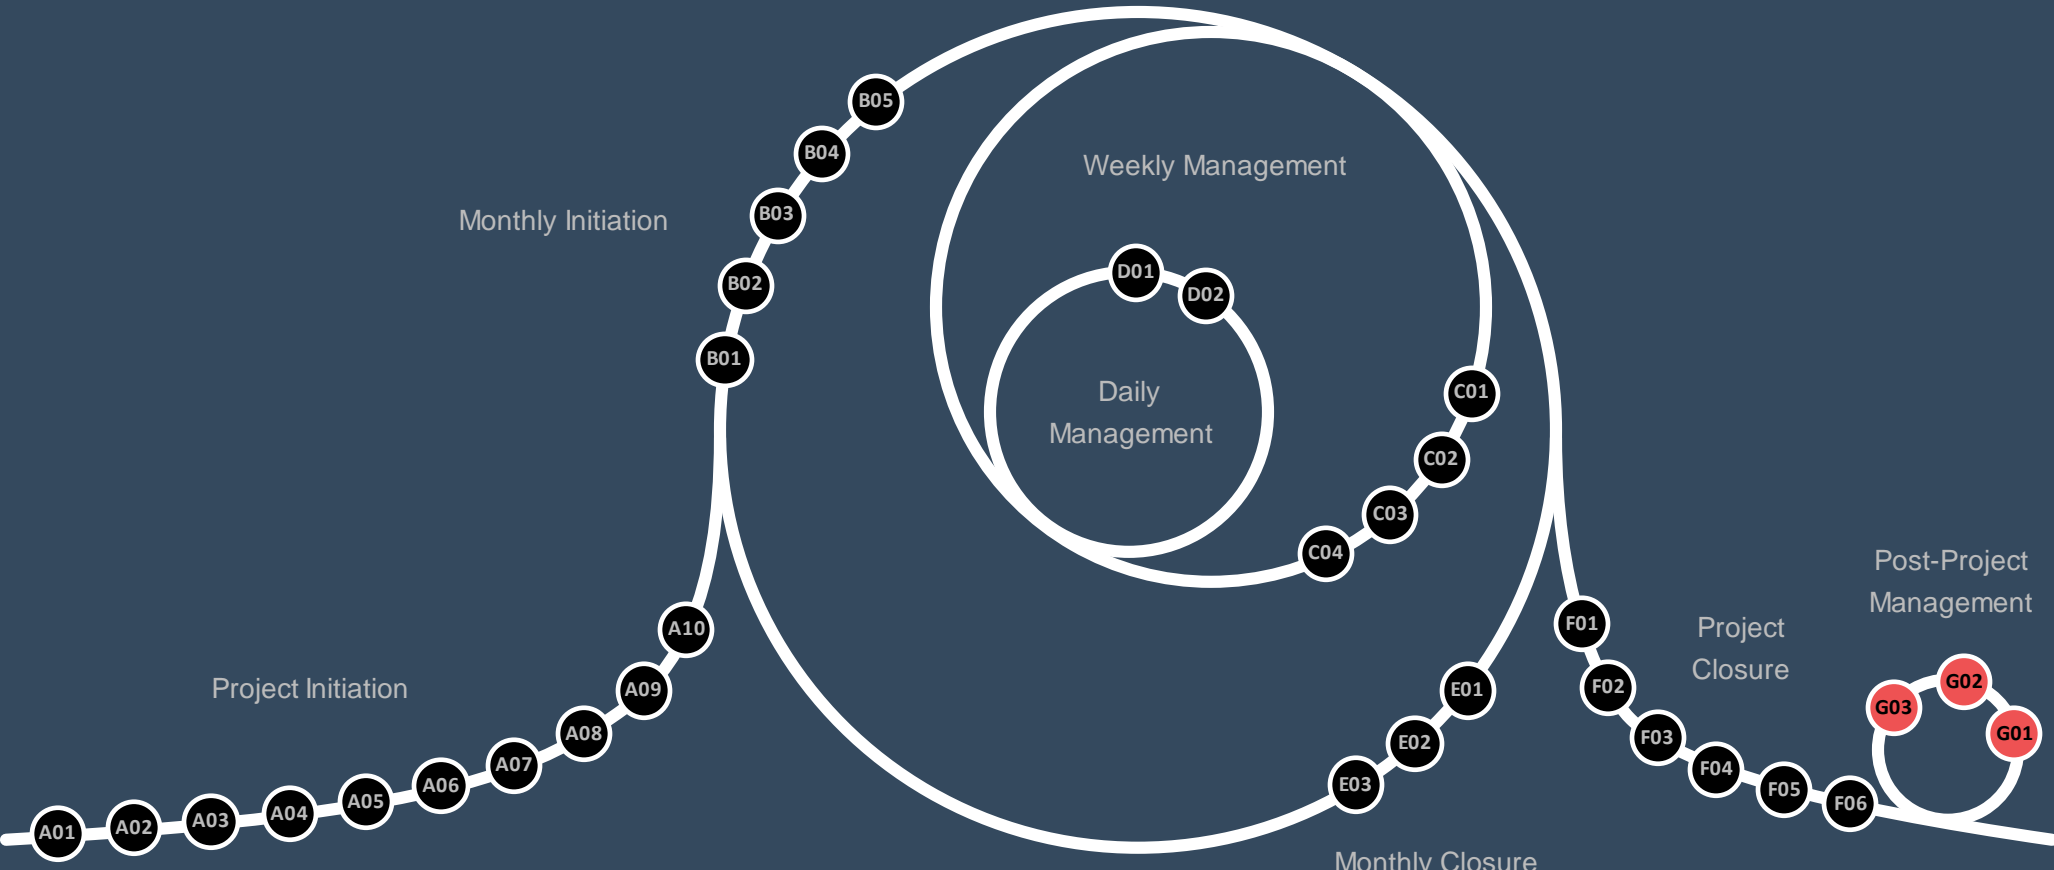

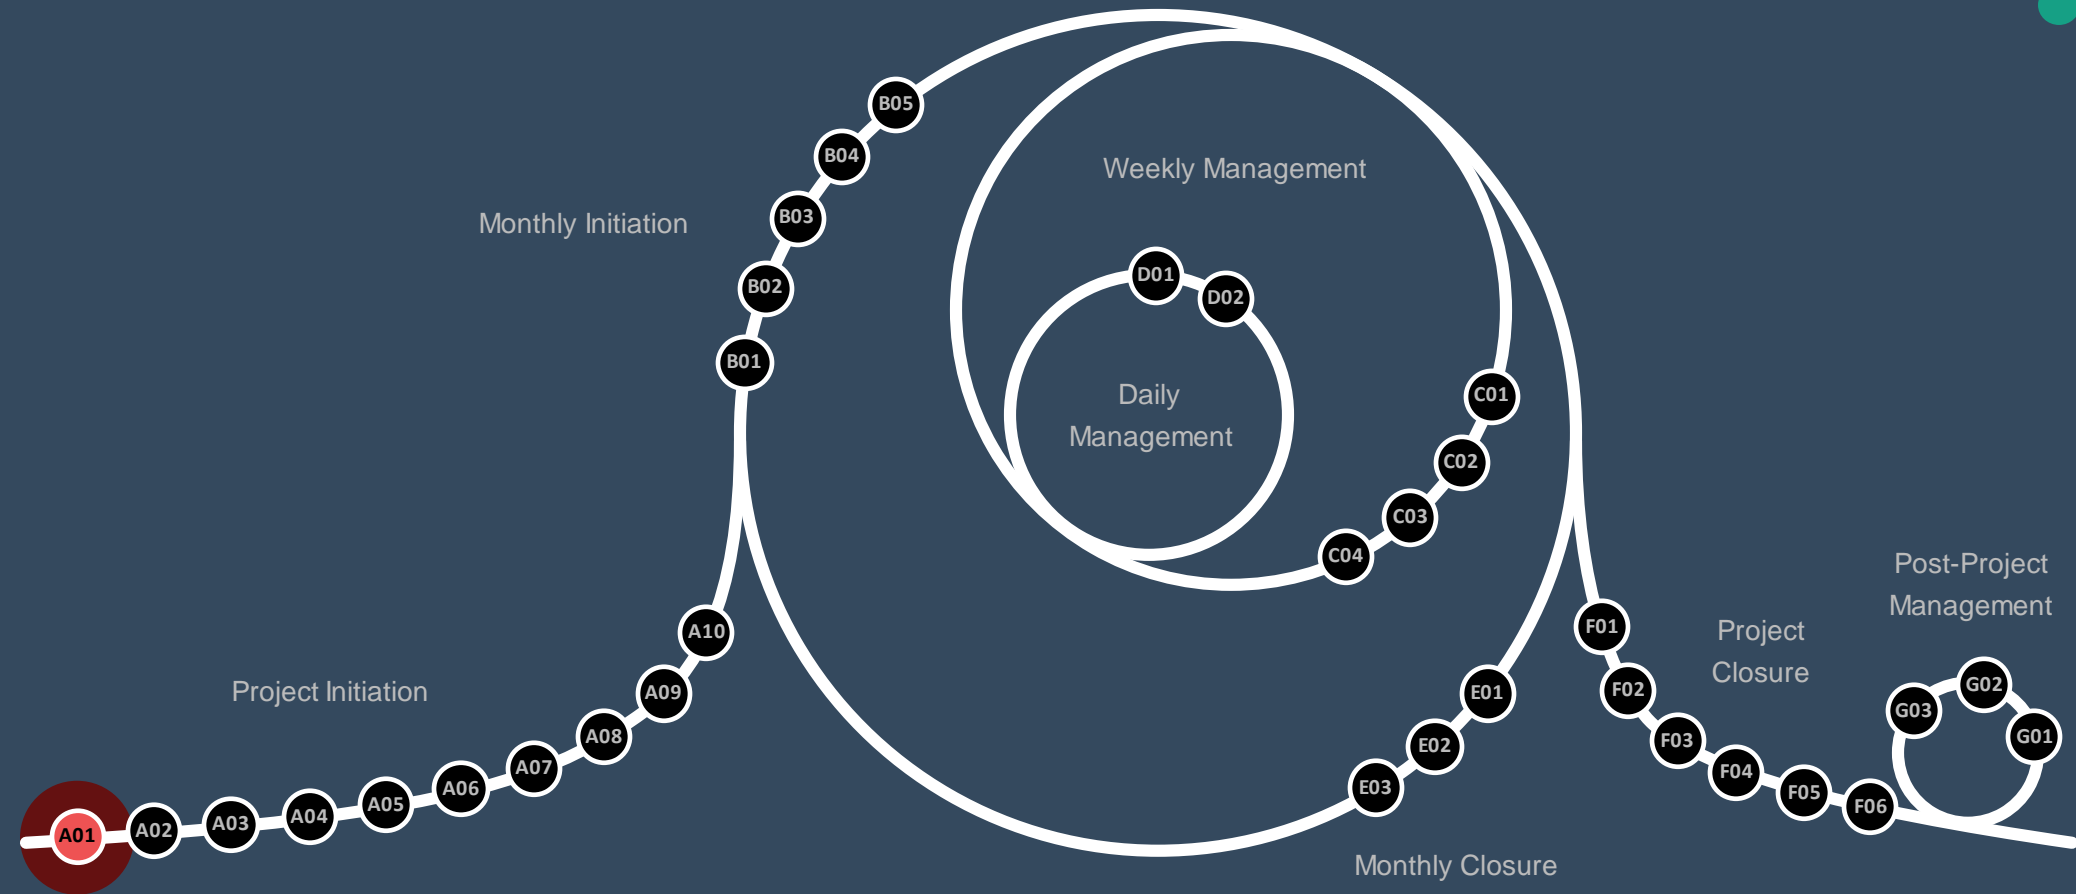


A01

Appoint the sponsor

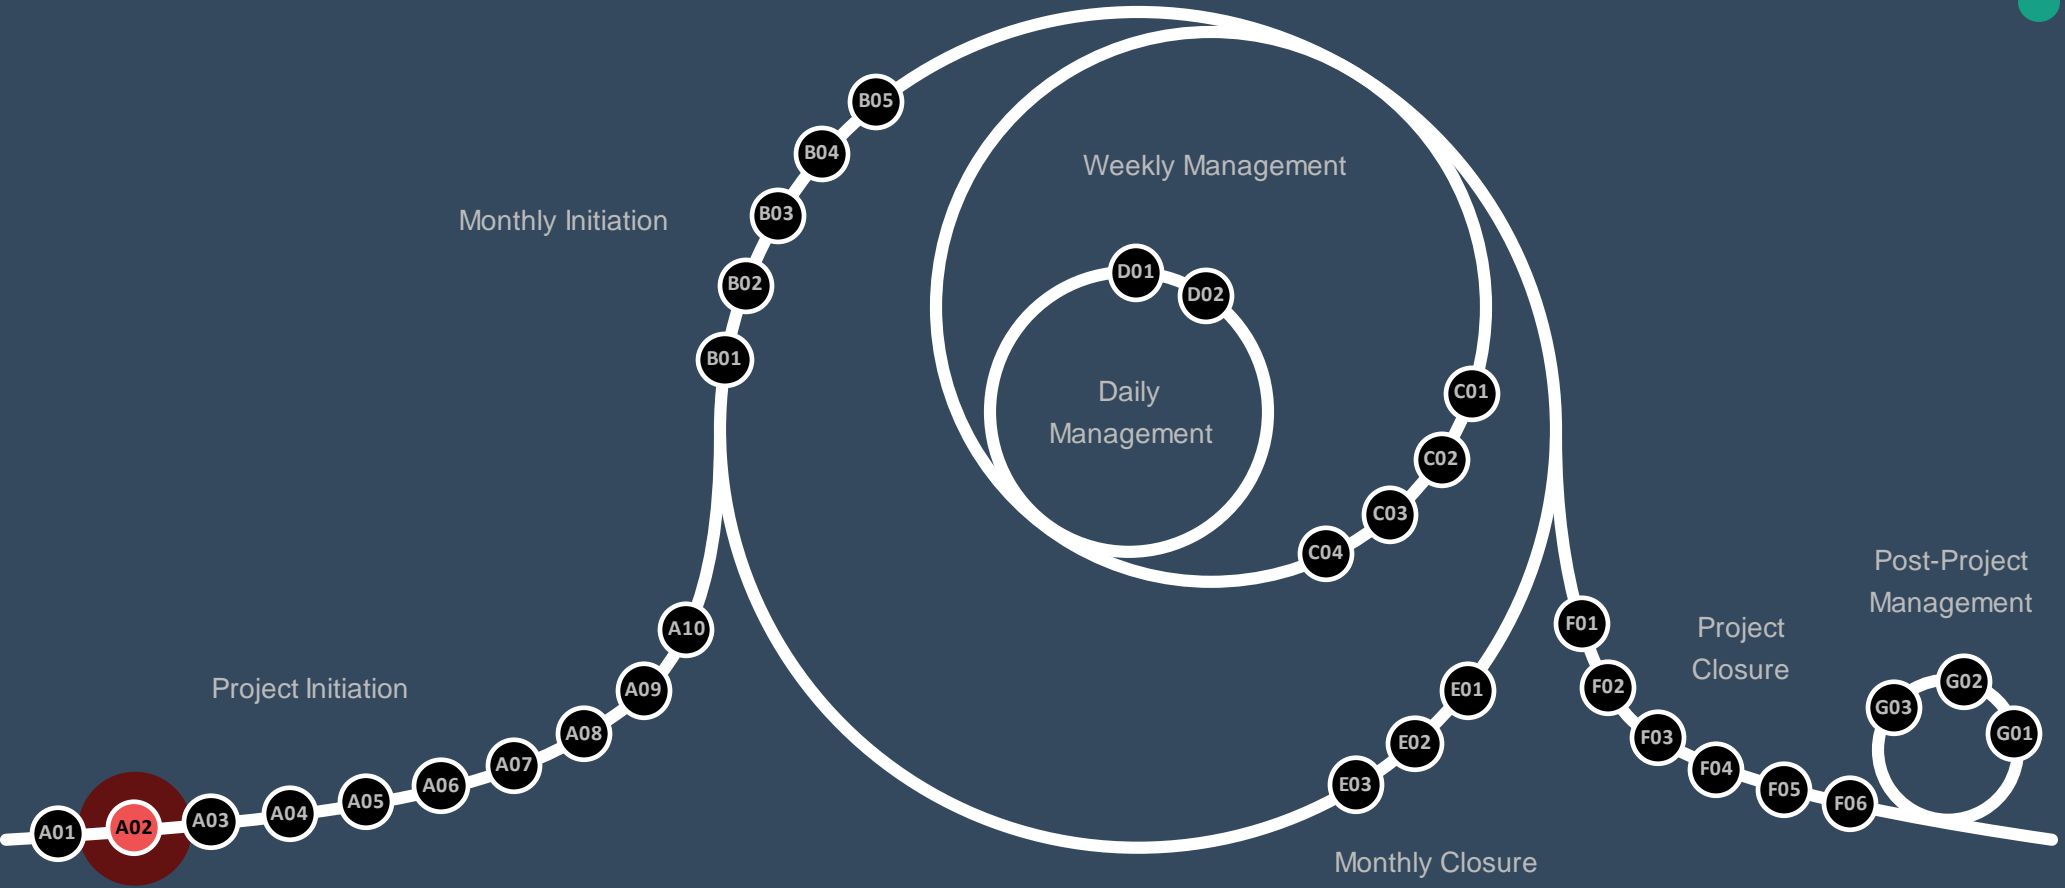

A02


Appoint the project manager

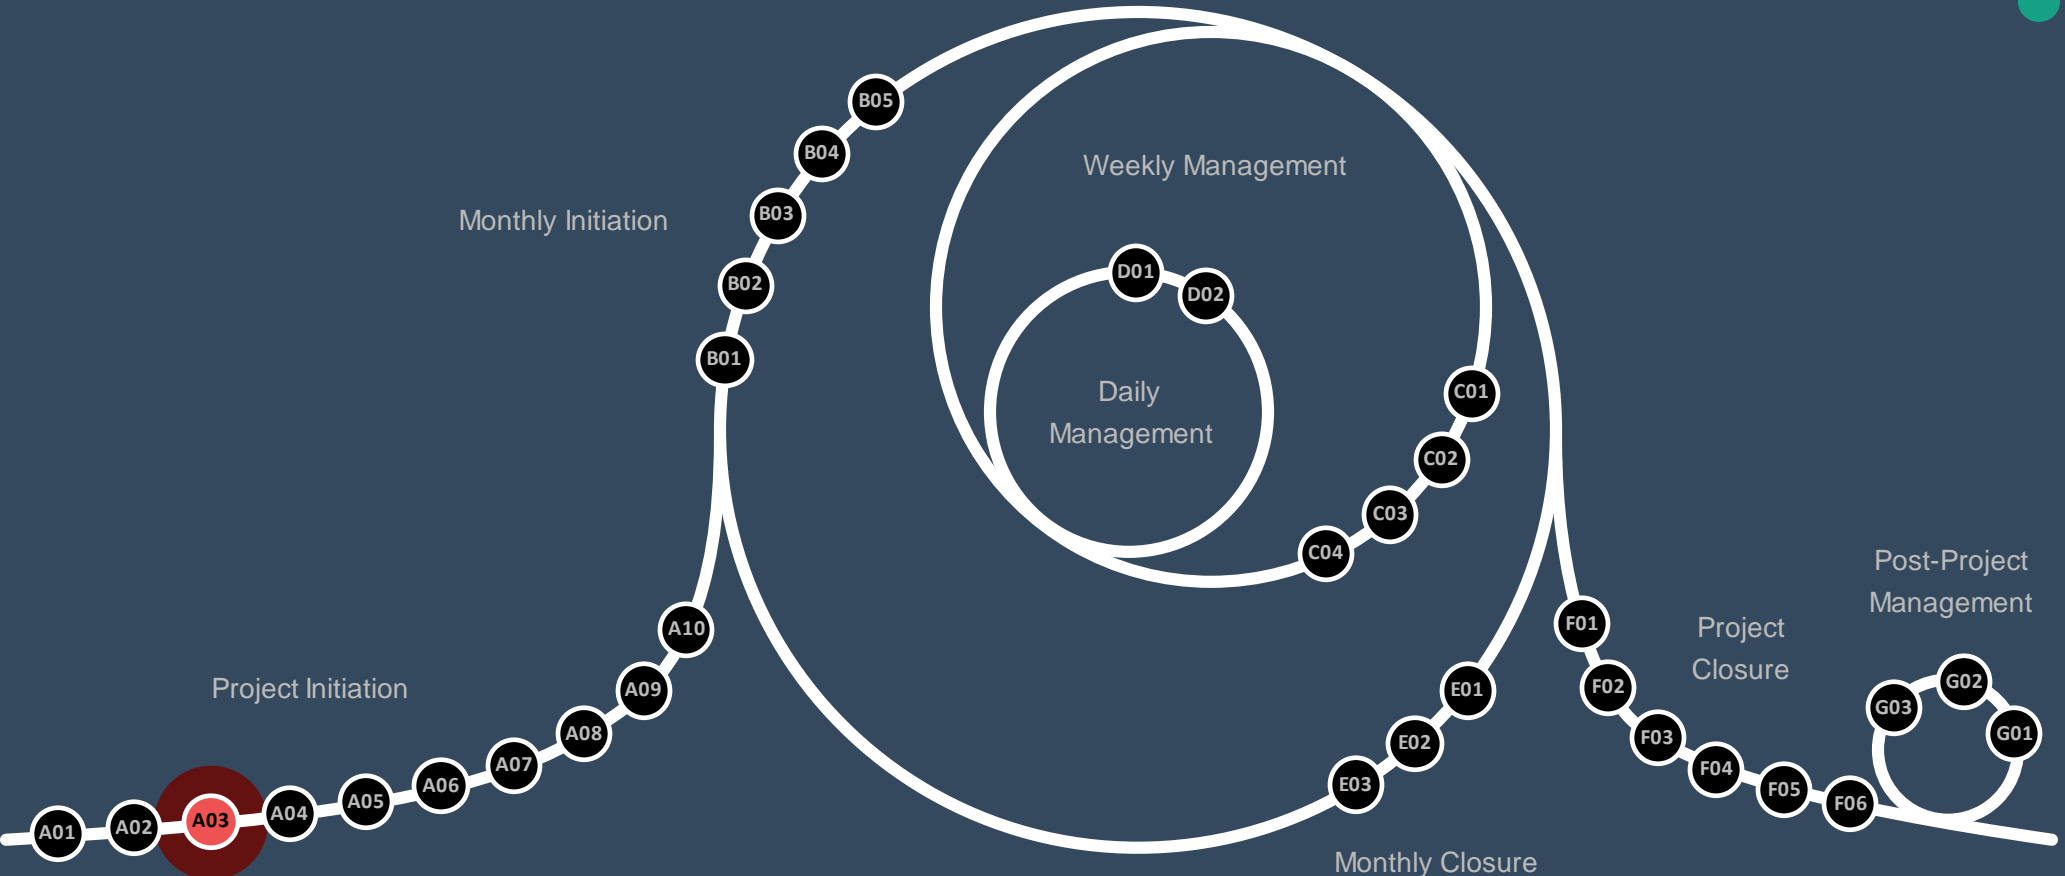

A03

Appoint the key team members

Project Description

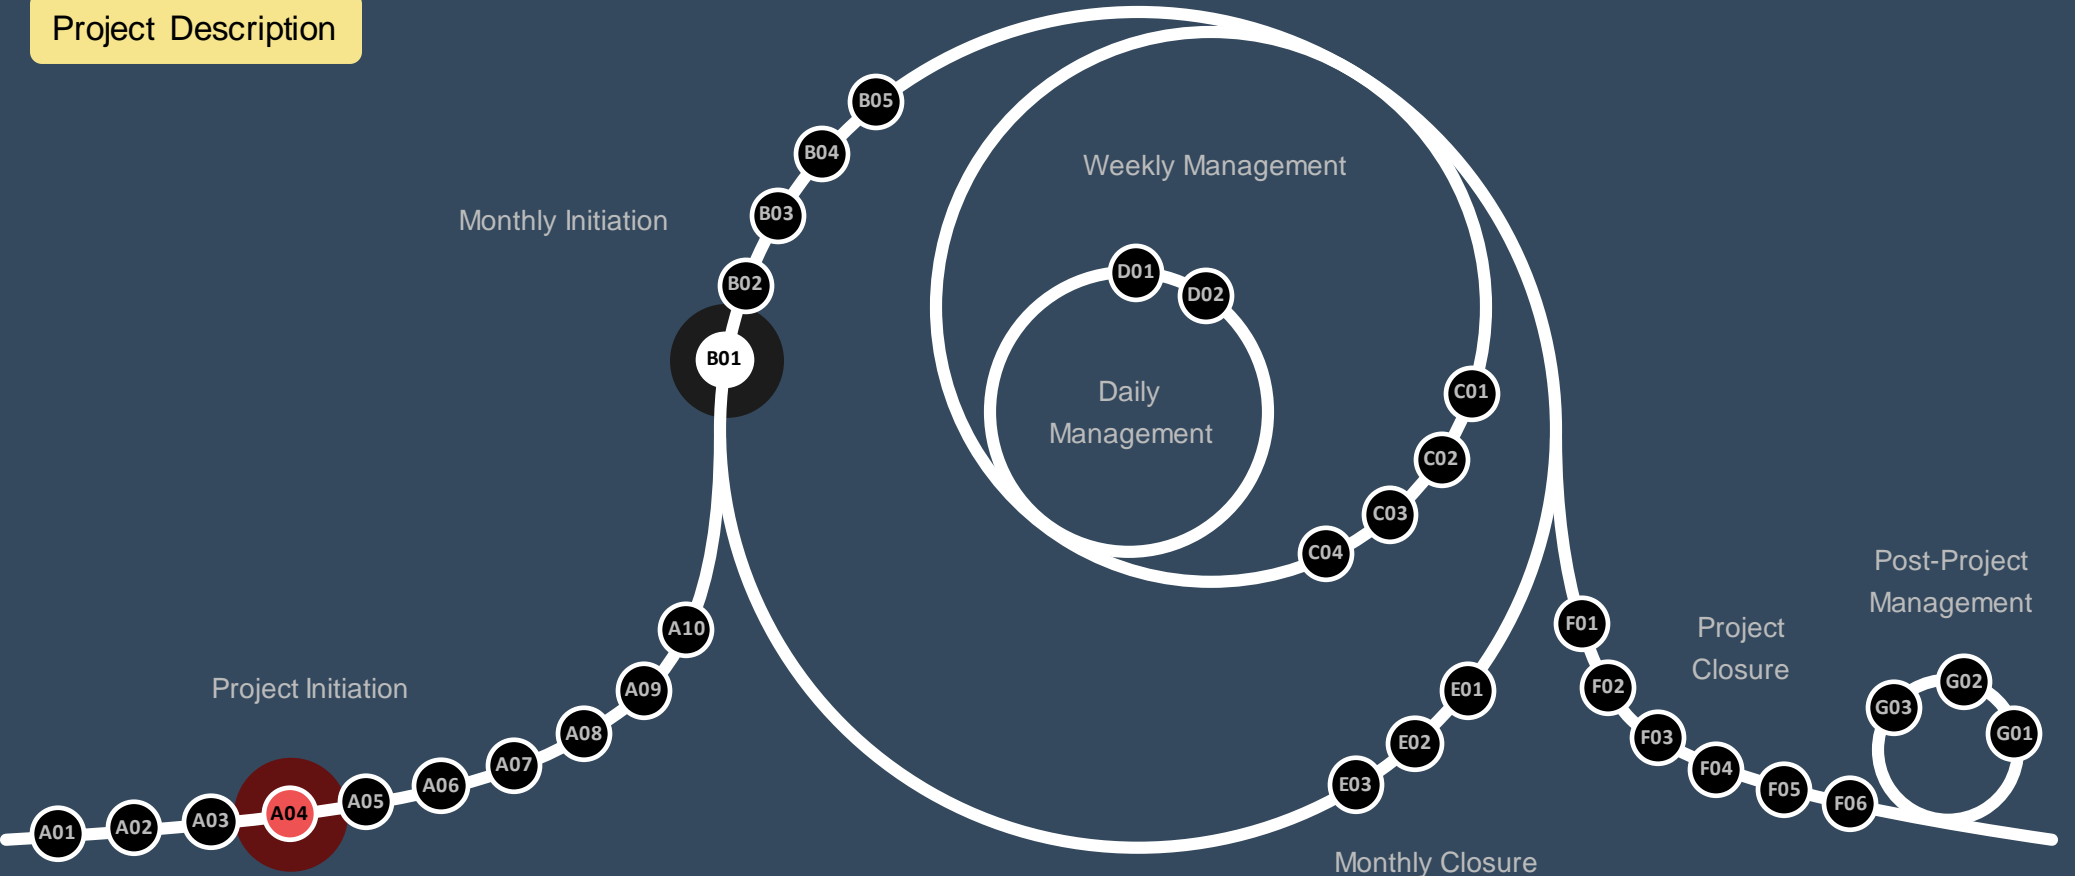


A04

Describe the project

Project Description

Deliverables Map

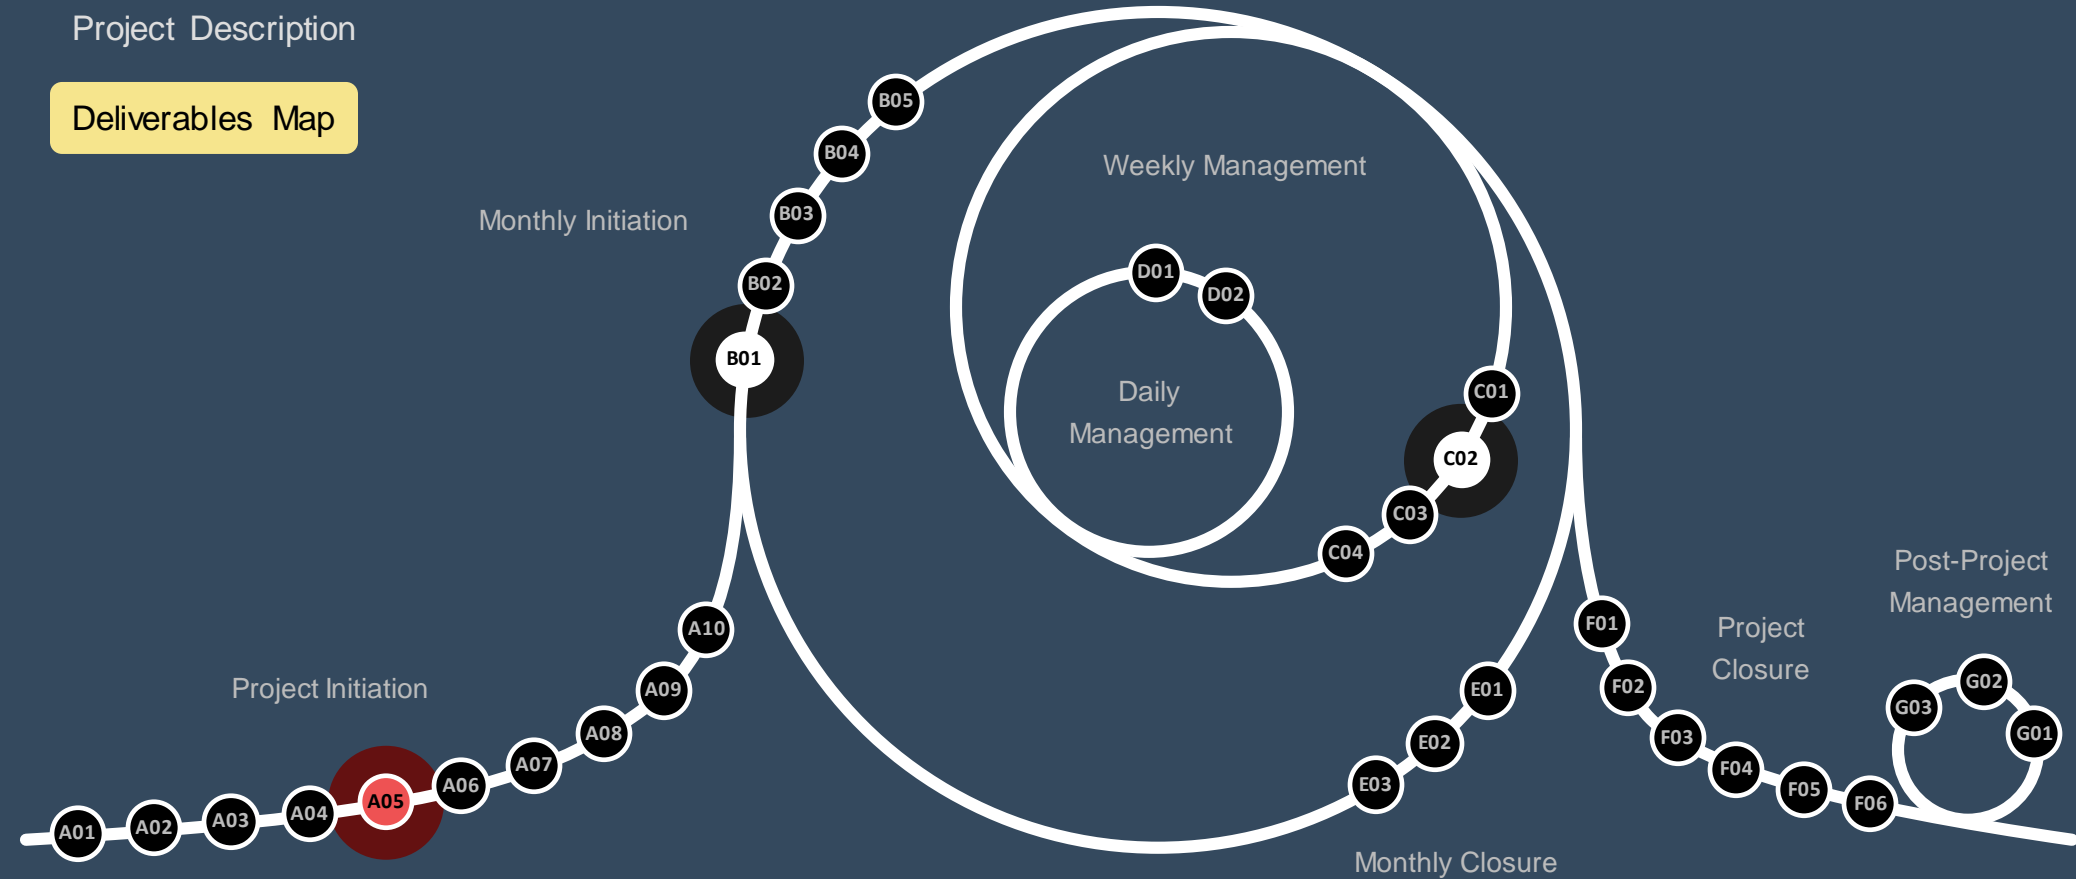

A05

Identify and plan the deliverables

Project Description

Deliverables Map

Follow-Up Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Project Closure

Post-Project Management

Monthly Closure

A06

Identify risks and plan responses

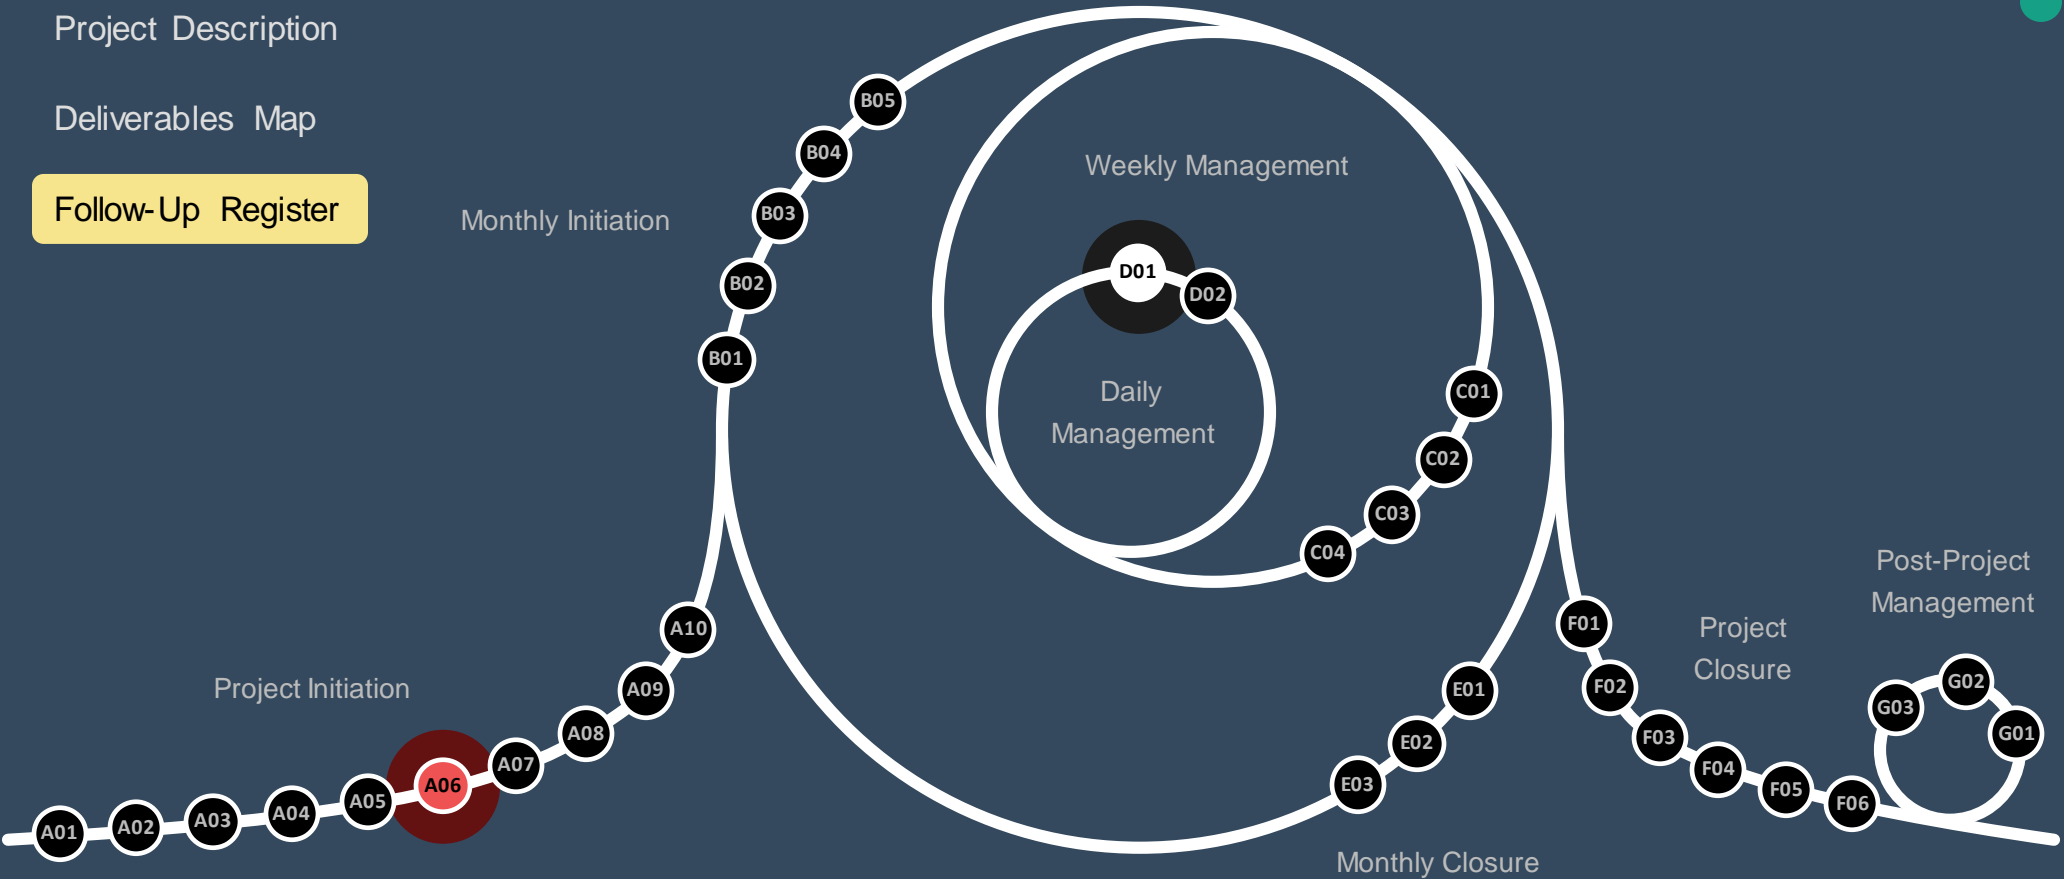


Project Description

Deliverables Map

Follow-Up Register

Health Register

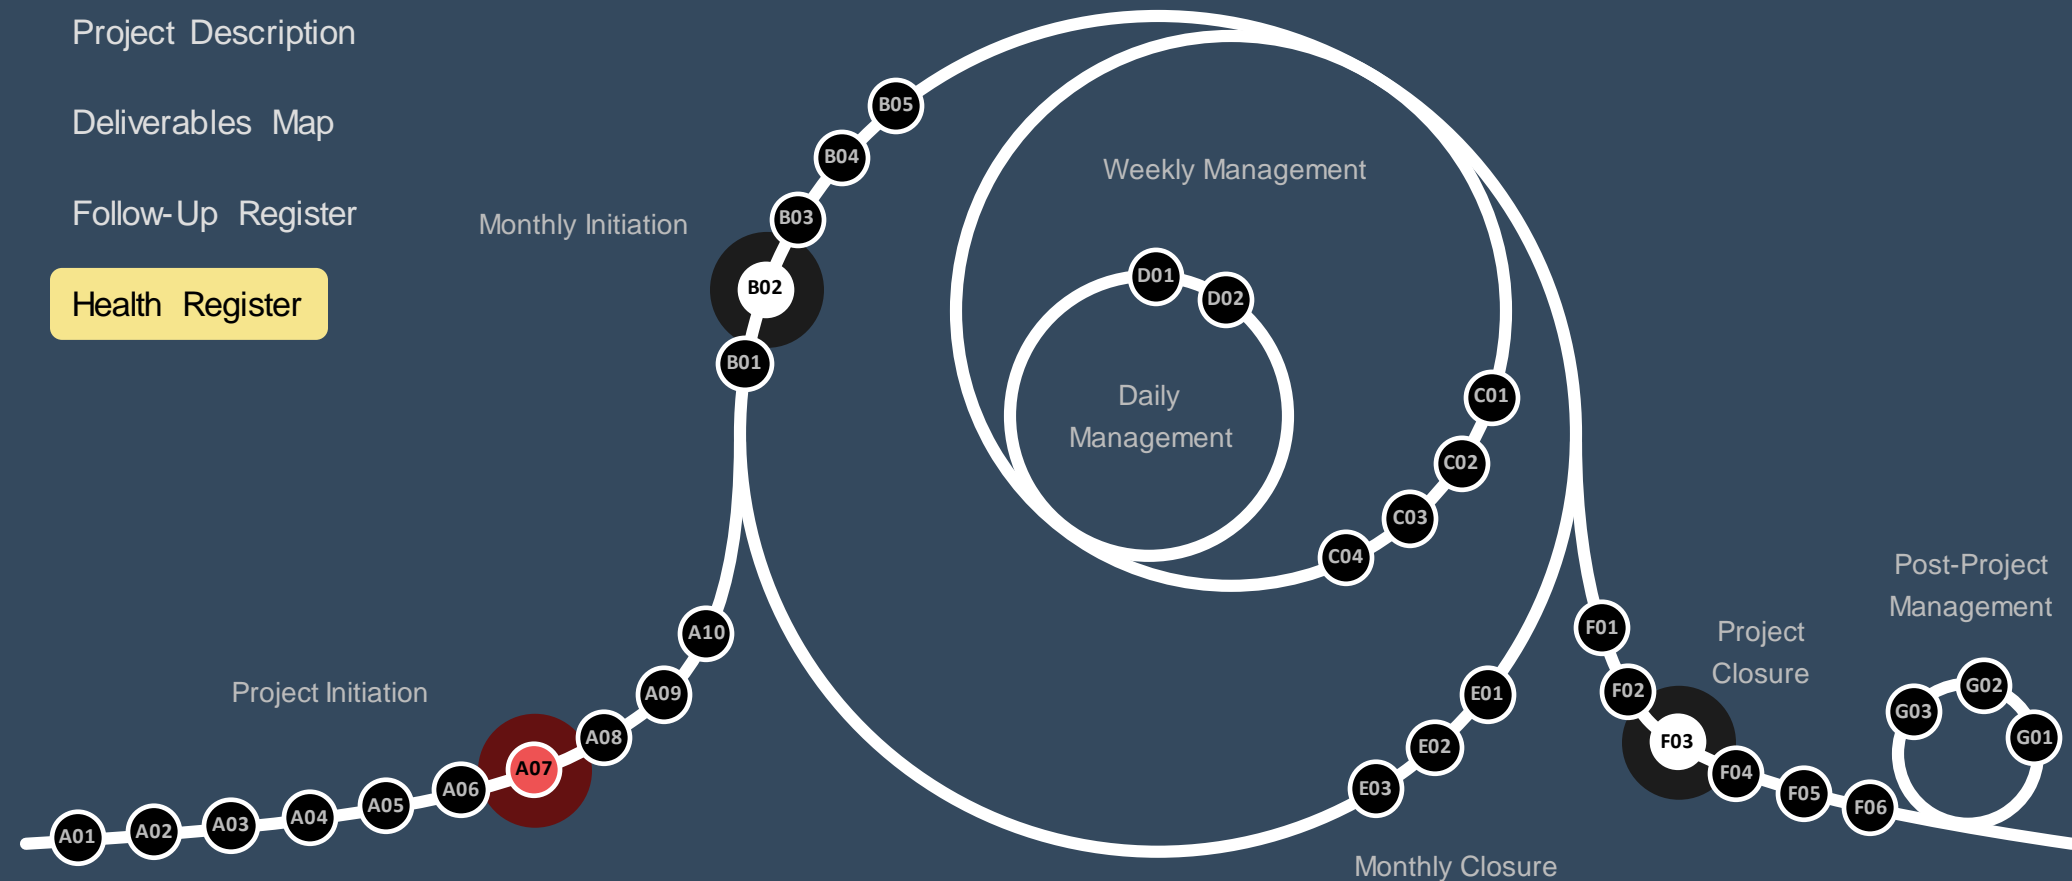

A07

Have project initiation peer-reviewed

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Project Closure

Post-Project Management

Monthly Closure

A08

Make a go/no-go decision

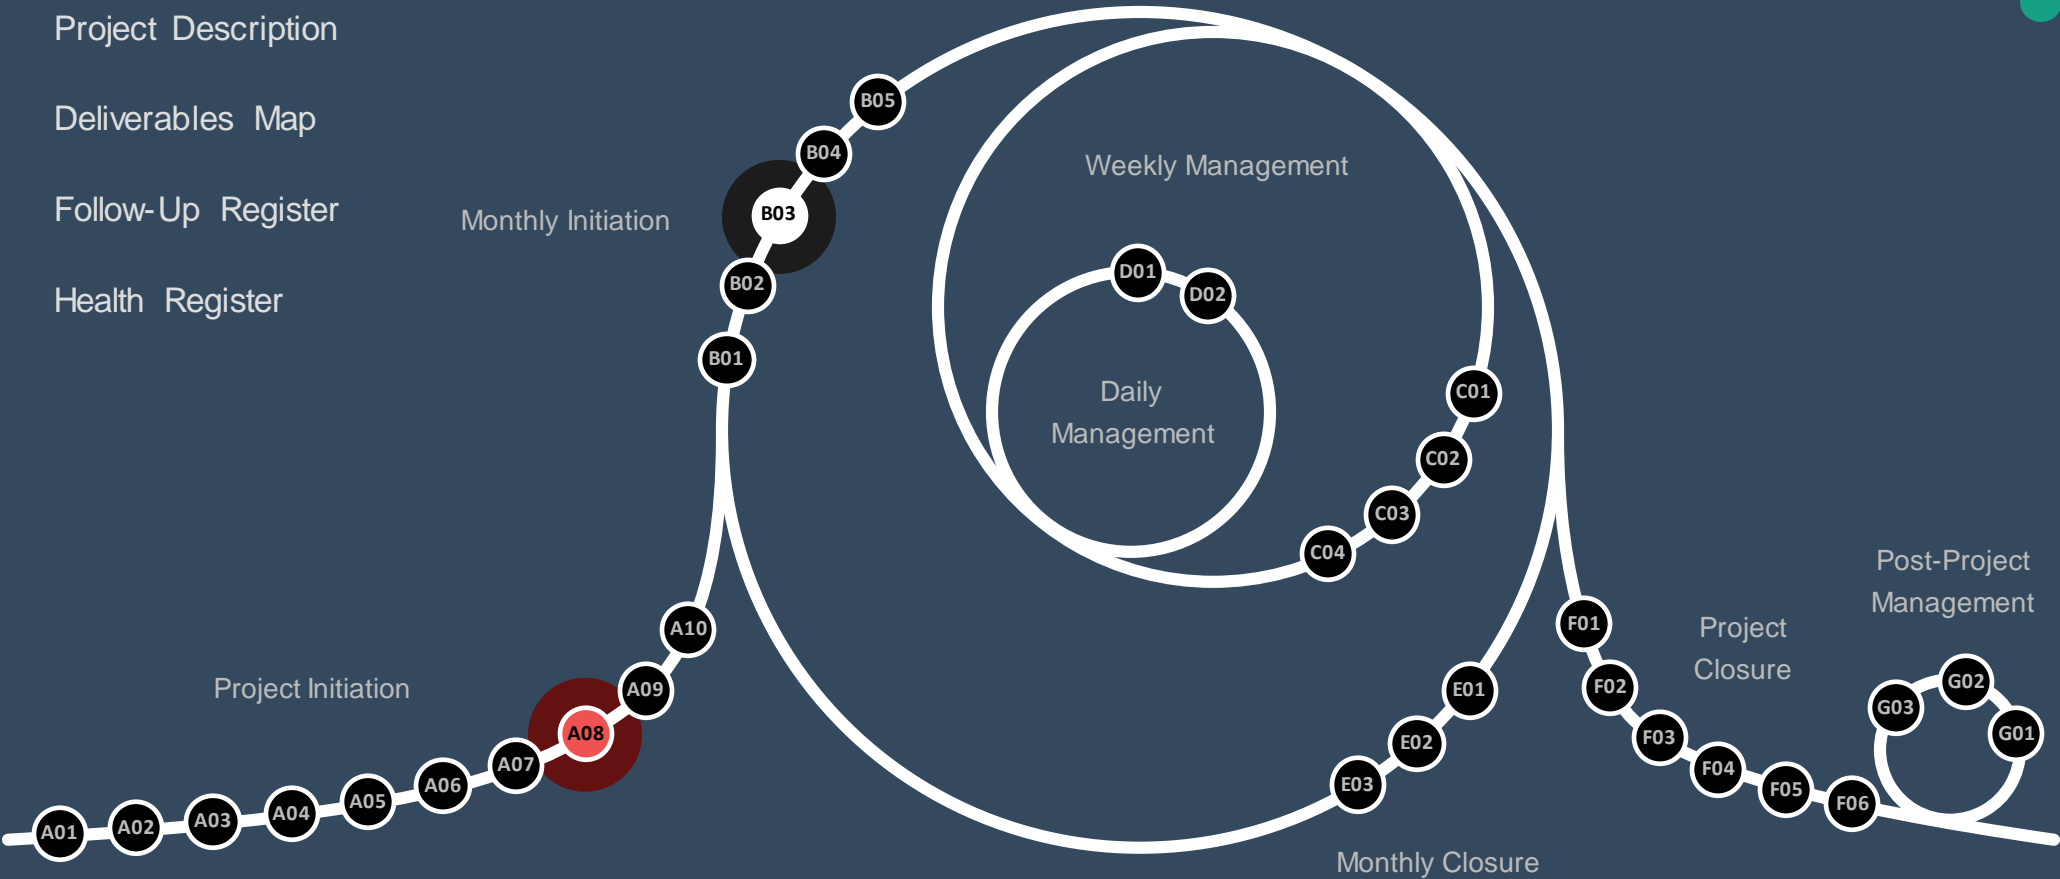

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Project Closure

Post-Project Management

Monthly Closure

A09

Kick off the project

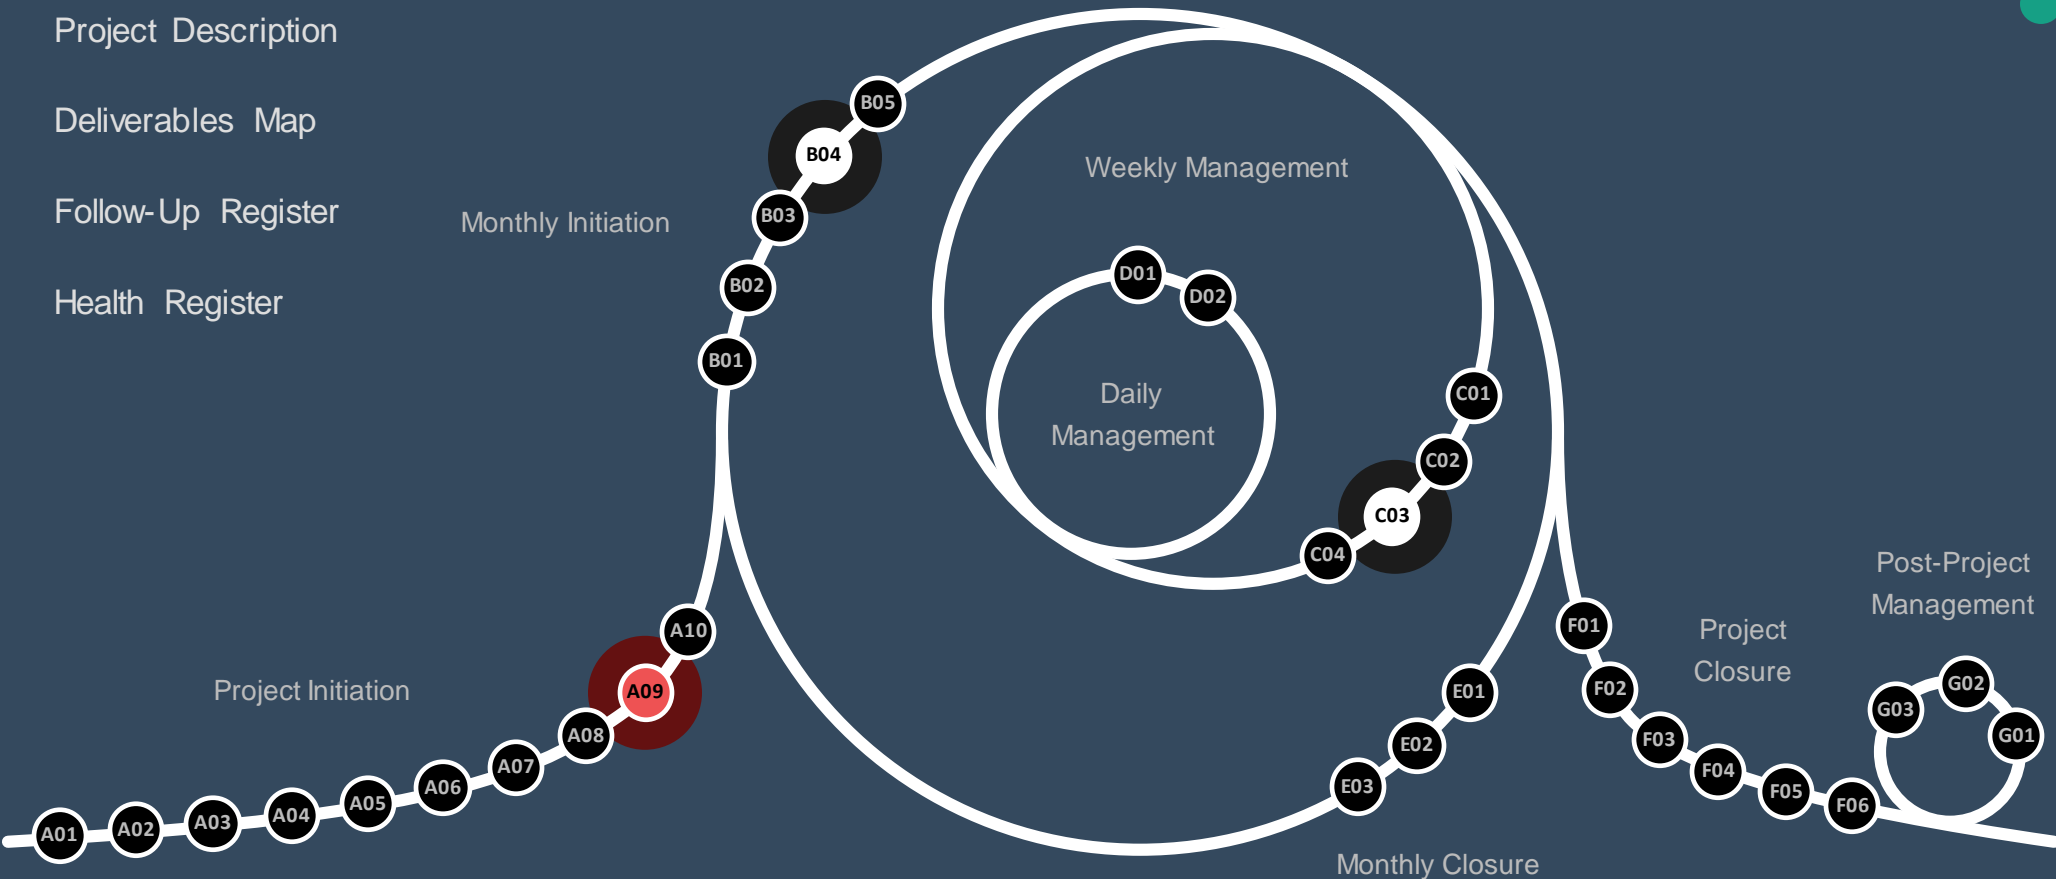

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation

Monthly Closure

Project Closure

Post-Project Management

A01

A02

A03

A04

A05

A06

A07

A08

A09

A10

B01

B02

B03

B04

B05

C01

C02

C03

C04

D01

D02

E01

E02

E03

F01

F02

F03

F04

F05

F06

G01

G02

G03

A10


Conduct a focused communication

Project Description

Deliverables Map

Follow-Up Register

Health Register

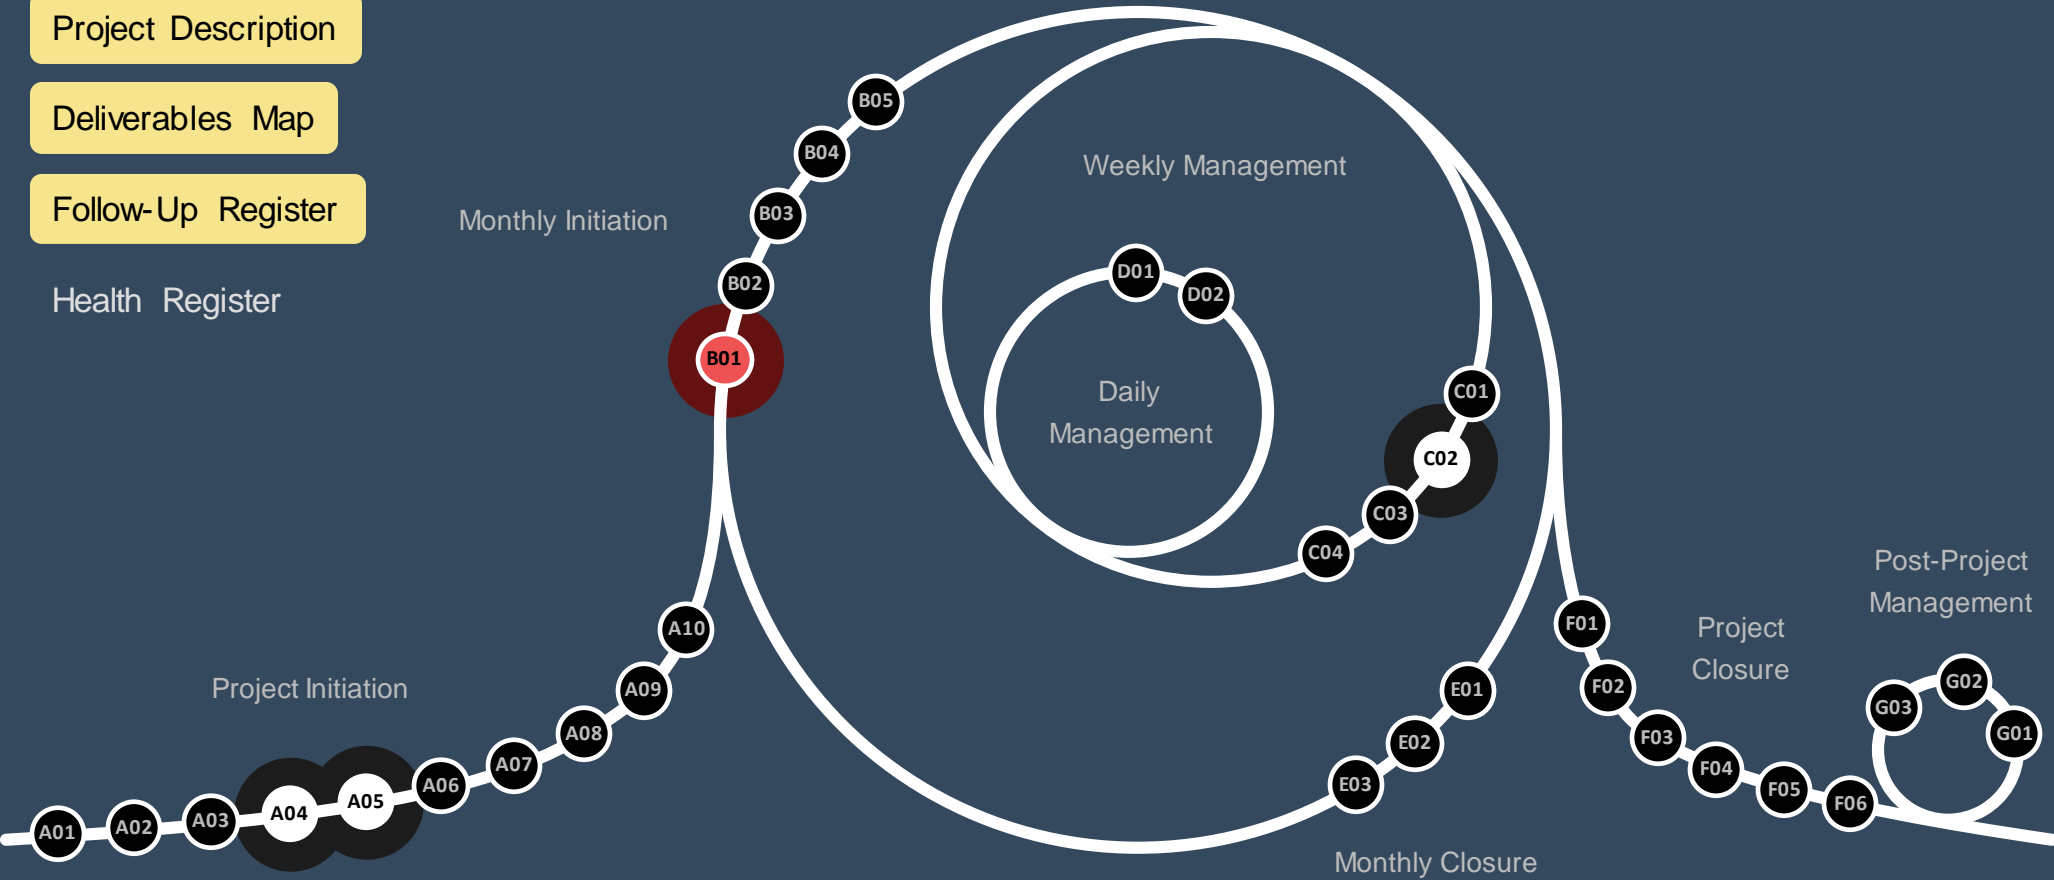

B01

Revise and refine the plans

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Project Closure

Post-Project Management

Monthly Closure

B02

Have the monthly cycle peer-reviewed

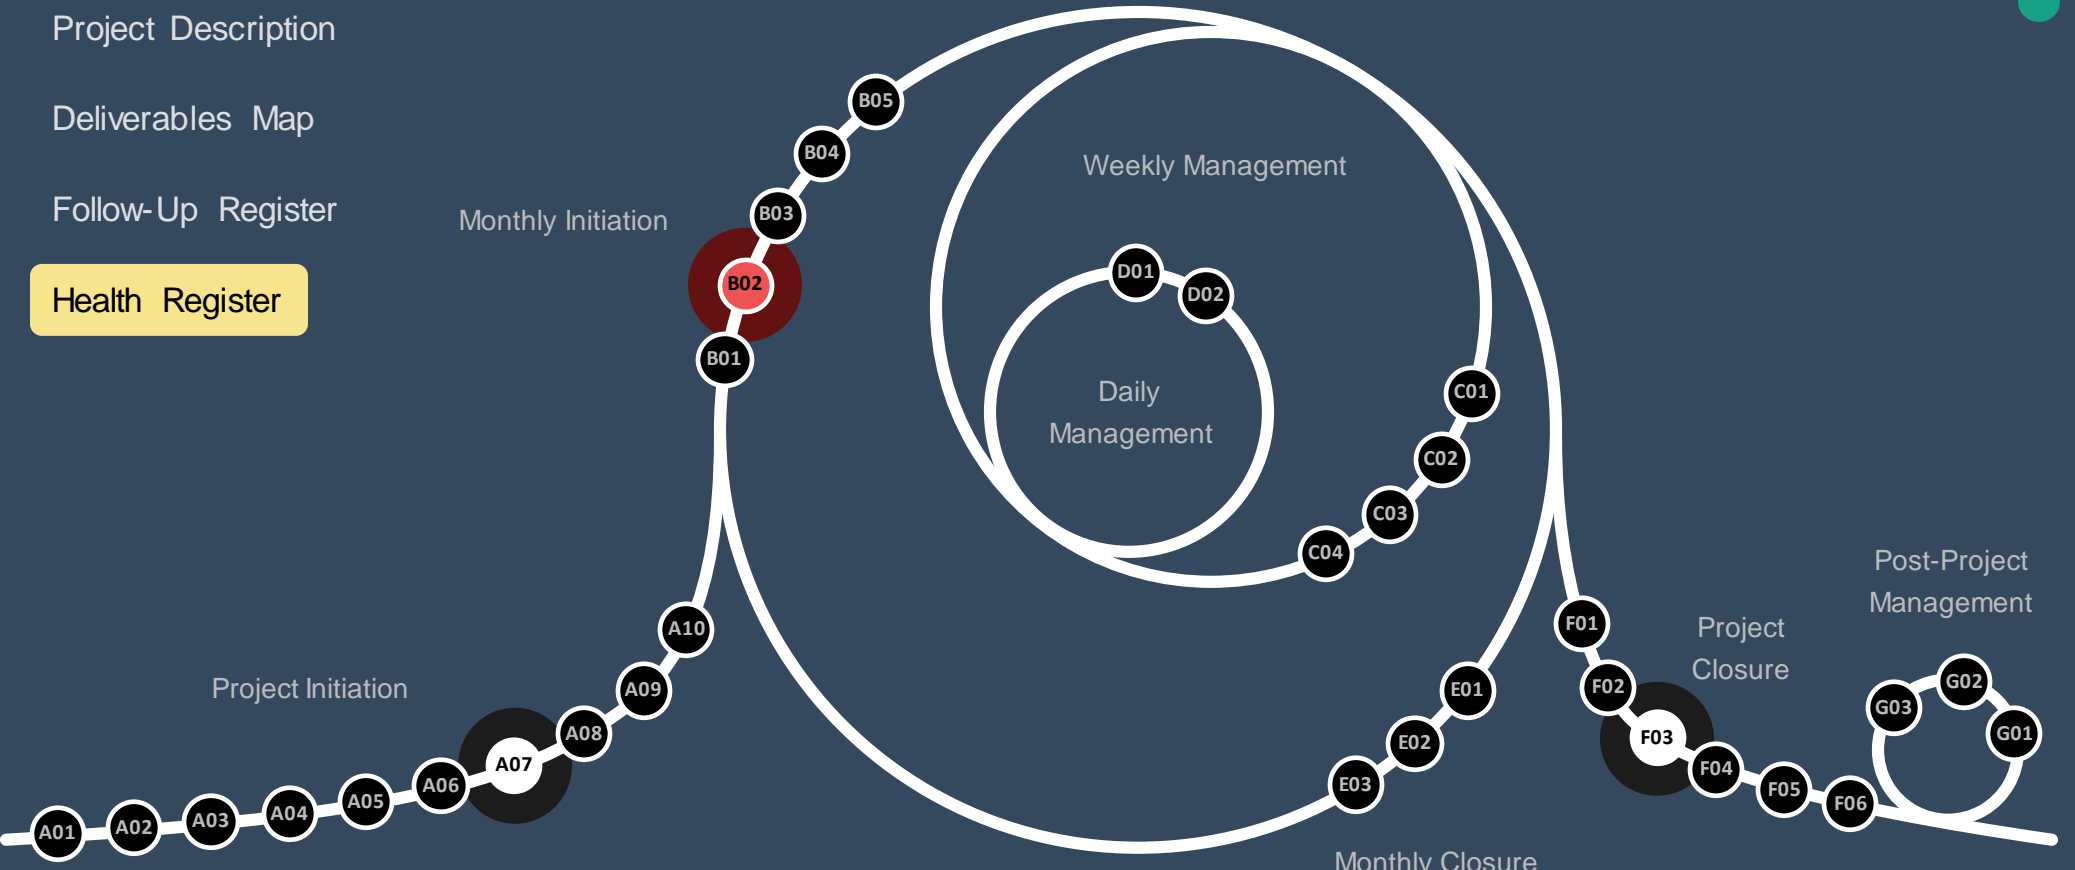

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Project Closure

Post-Project Management

Monthly Closure

B03

Make a go/no-go decision

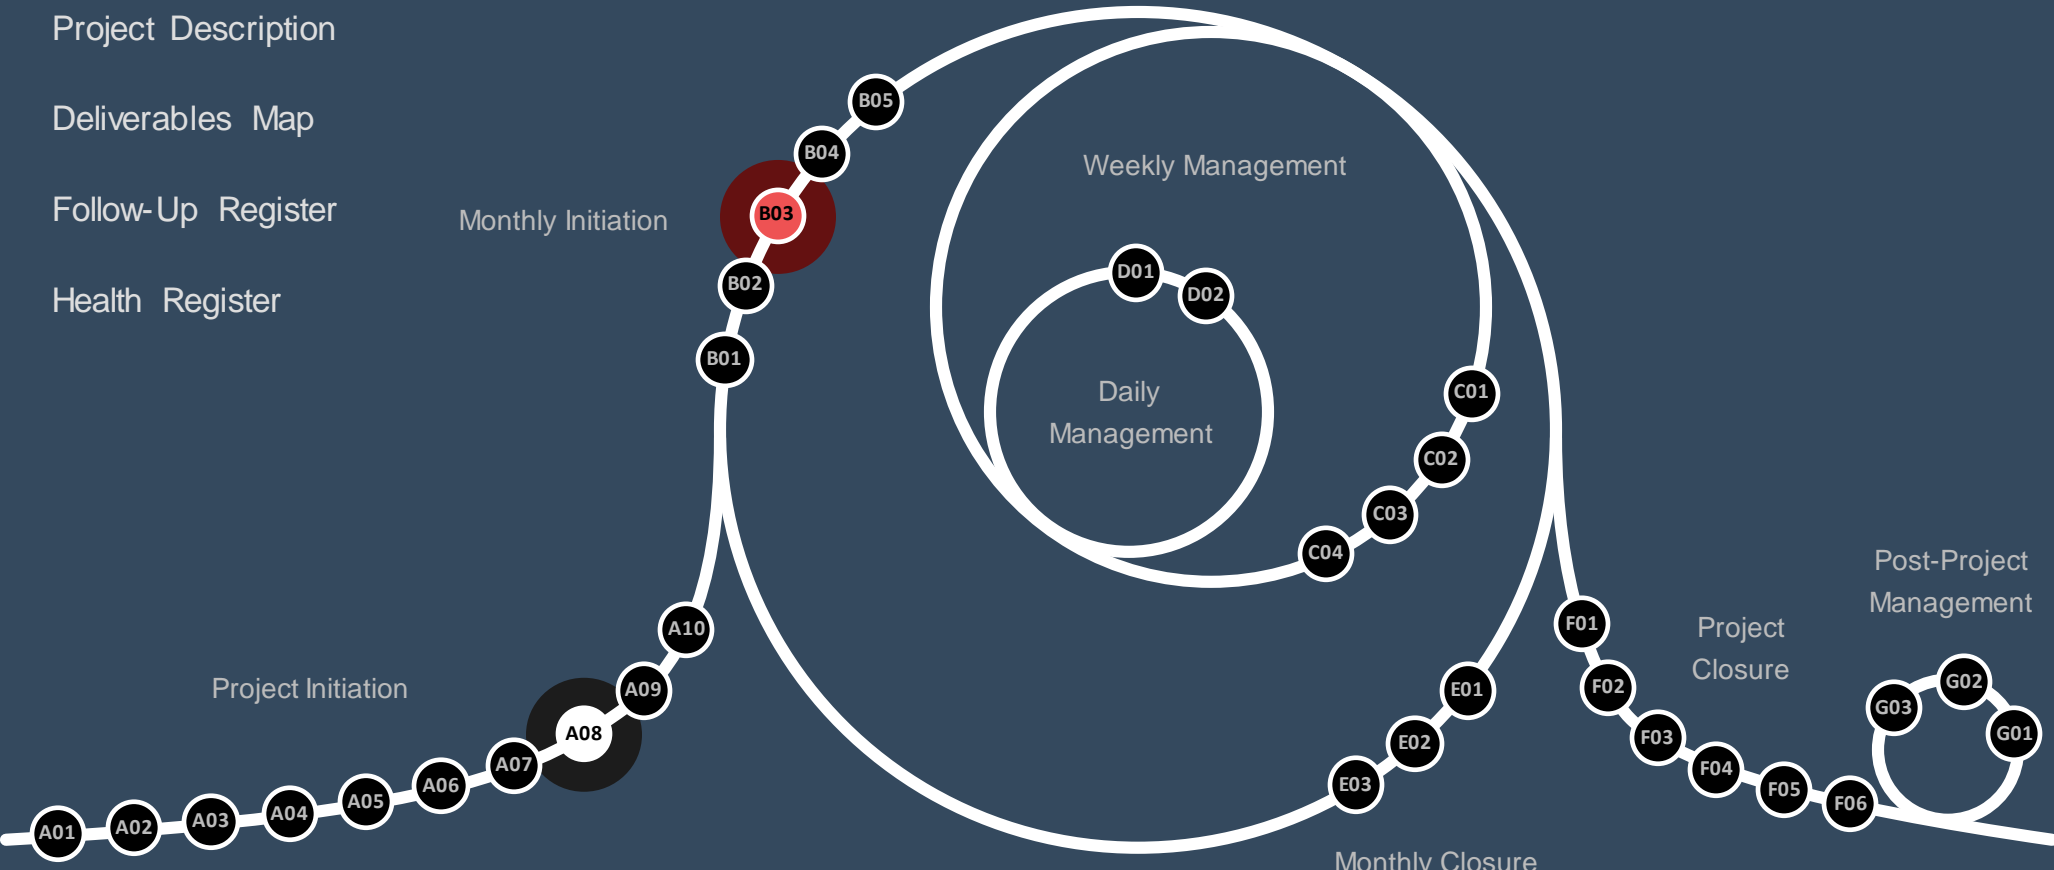

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Project Closure

Post-Project Management

Monthly Closure

B04

Kick off the monthly cycle

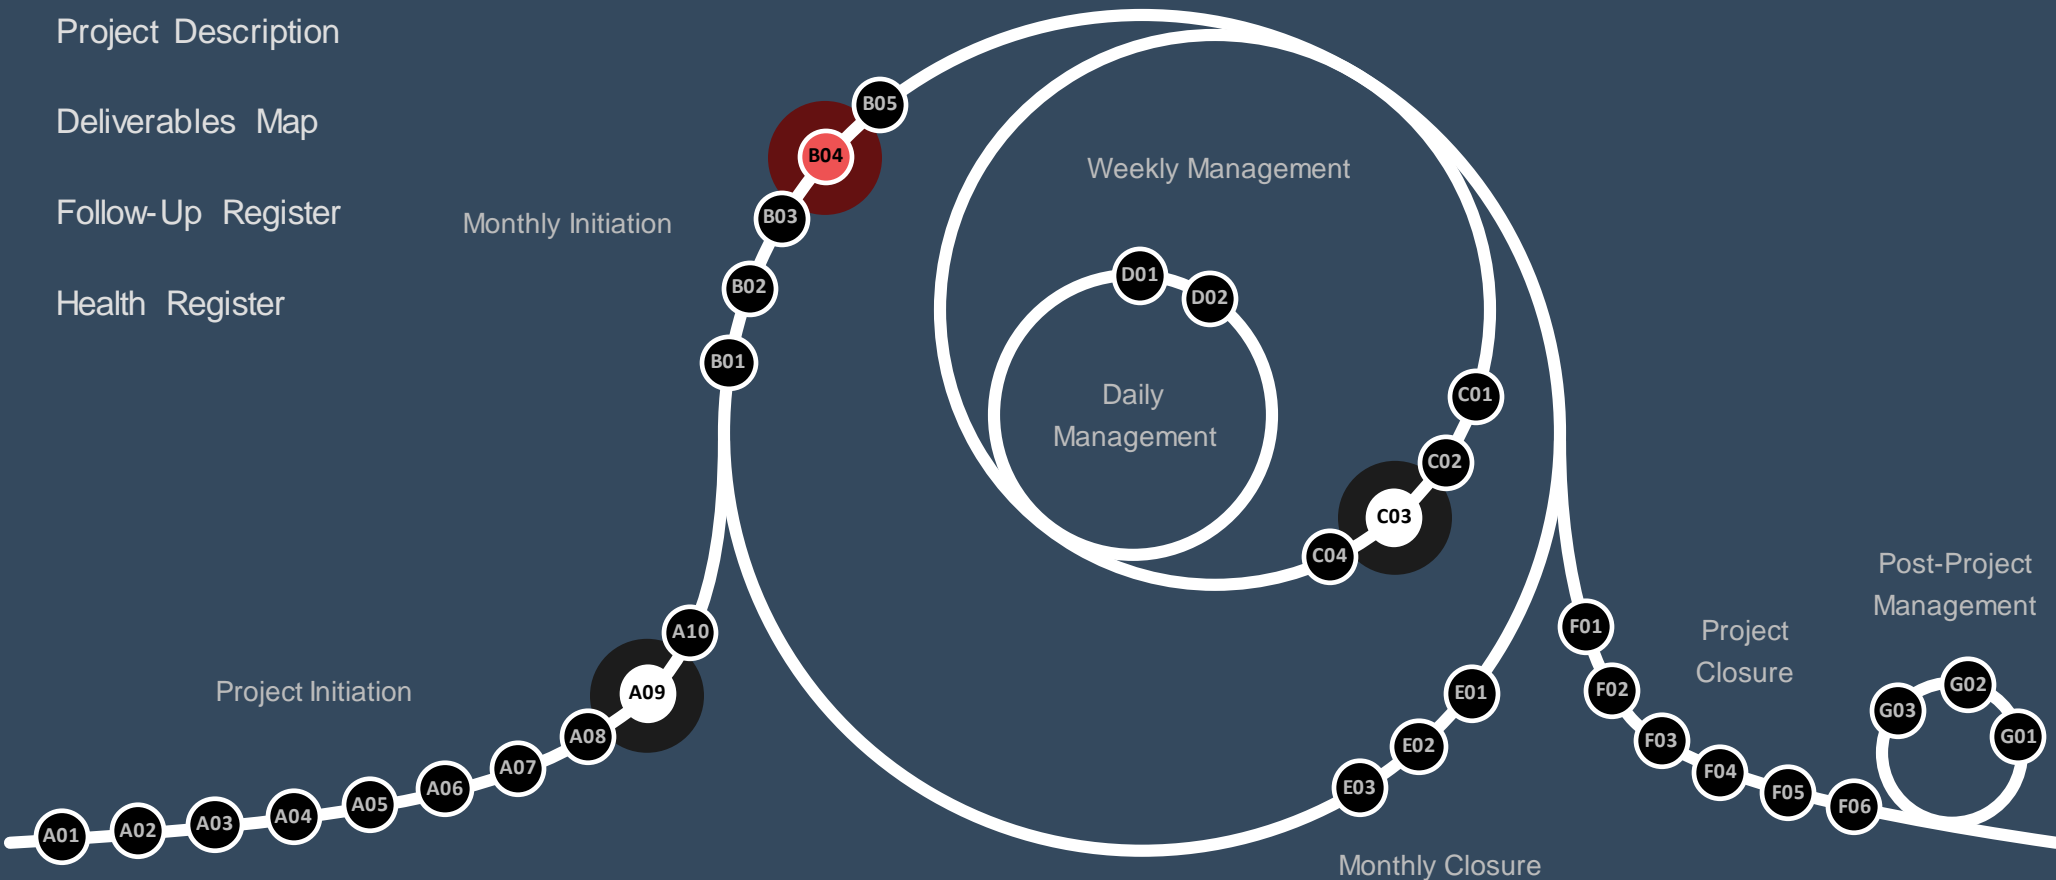

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Monthly Closure

Project Closure

Post-Project Management

B05

Conduct a focused communication

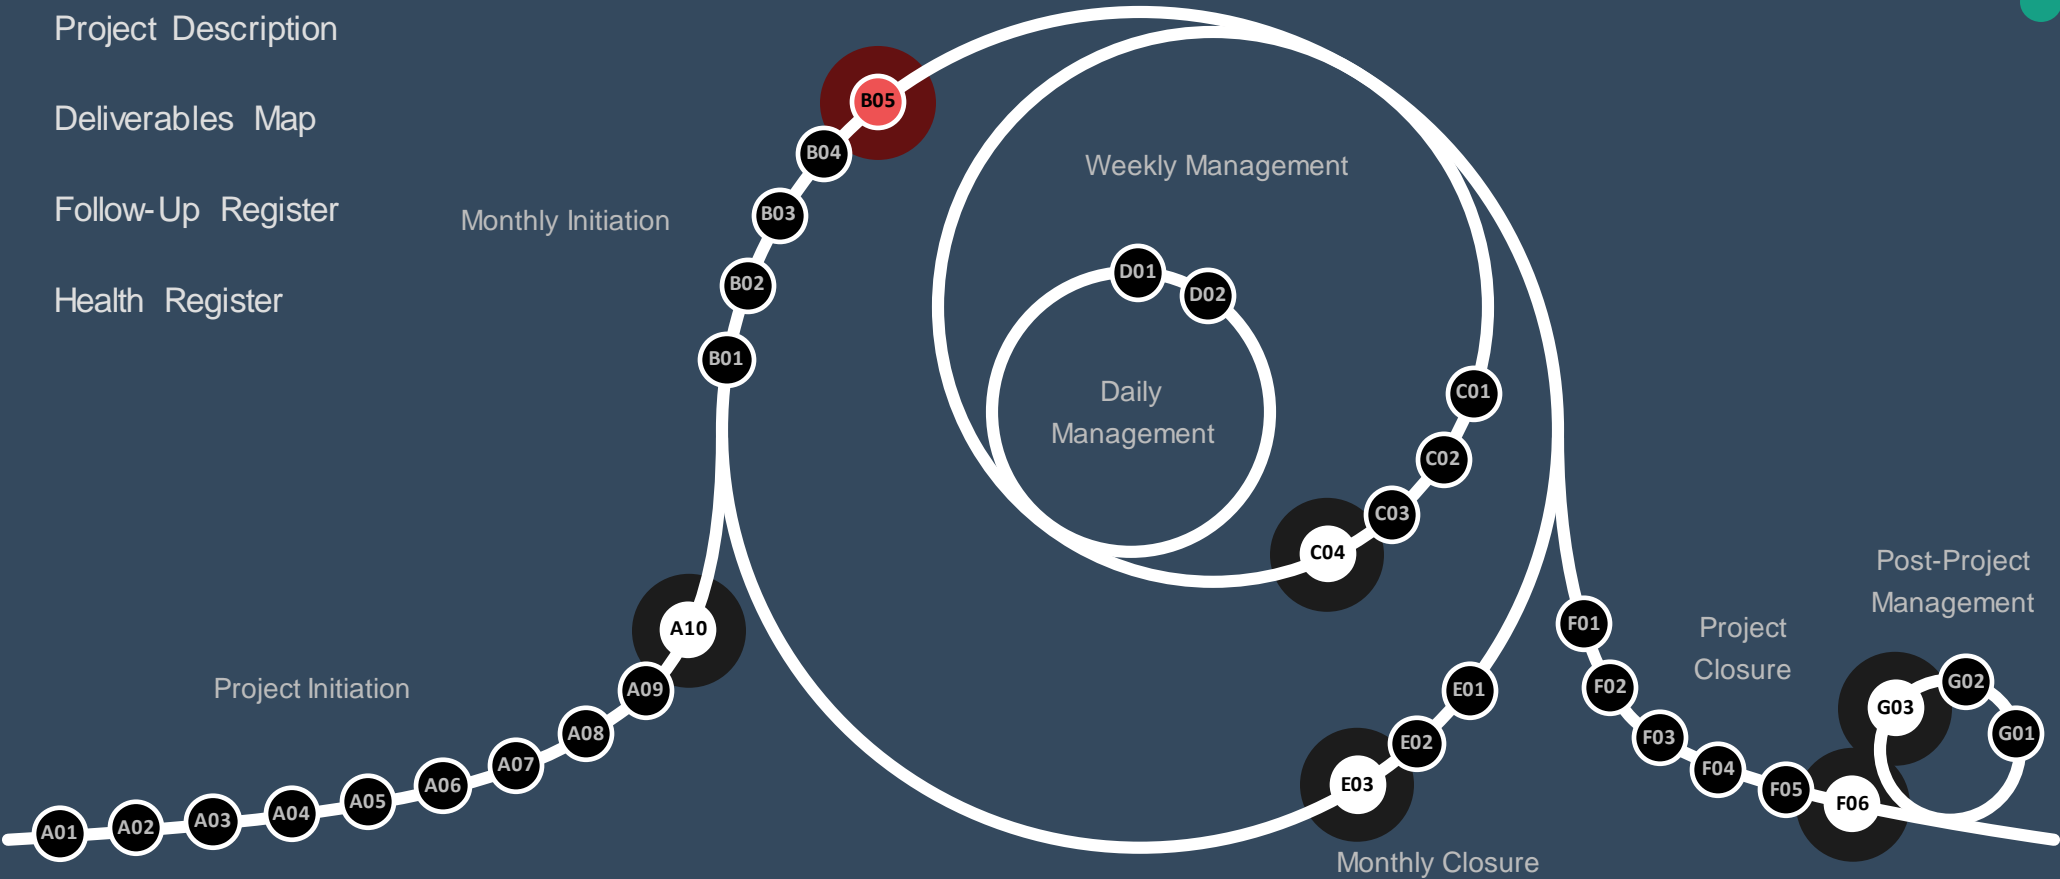

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation

Monthly Closure

Project Closure

Post-Project Management

A01

A02

A03

A04

A05

A06

A07

A08

A09

A10

B01

B02

B03

B04

B05

D01

D02

C01

C02

C03

C04

E01

E02

E03

F01

F02

F03

F04

F05

F06

G02

G01

G03

C01


Measure and report performance

Project Description

Deliverables Map

Follow-Up Register

Health Register

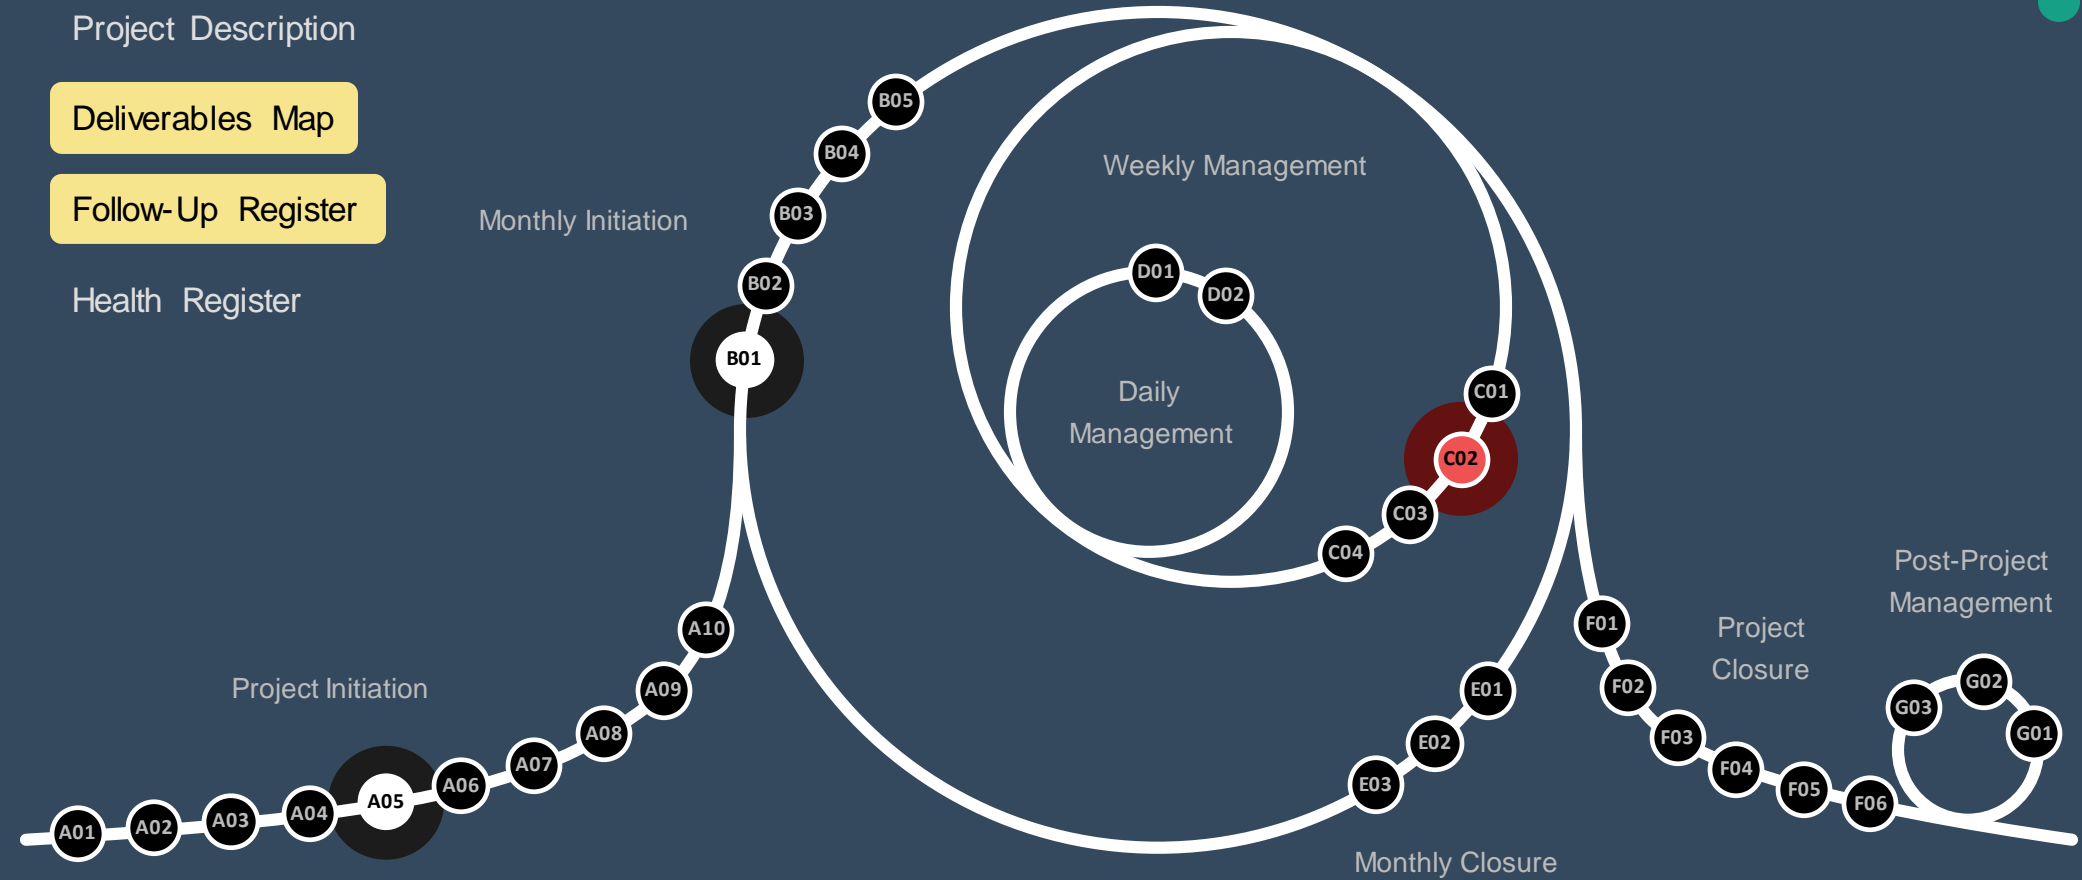

C02

Plan responses for deviations

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Project Closure

Post-Project Management

Monthly Closure

C03

Kick off the weekly cycle

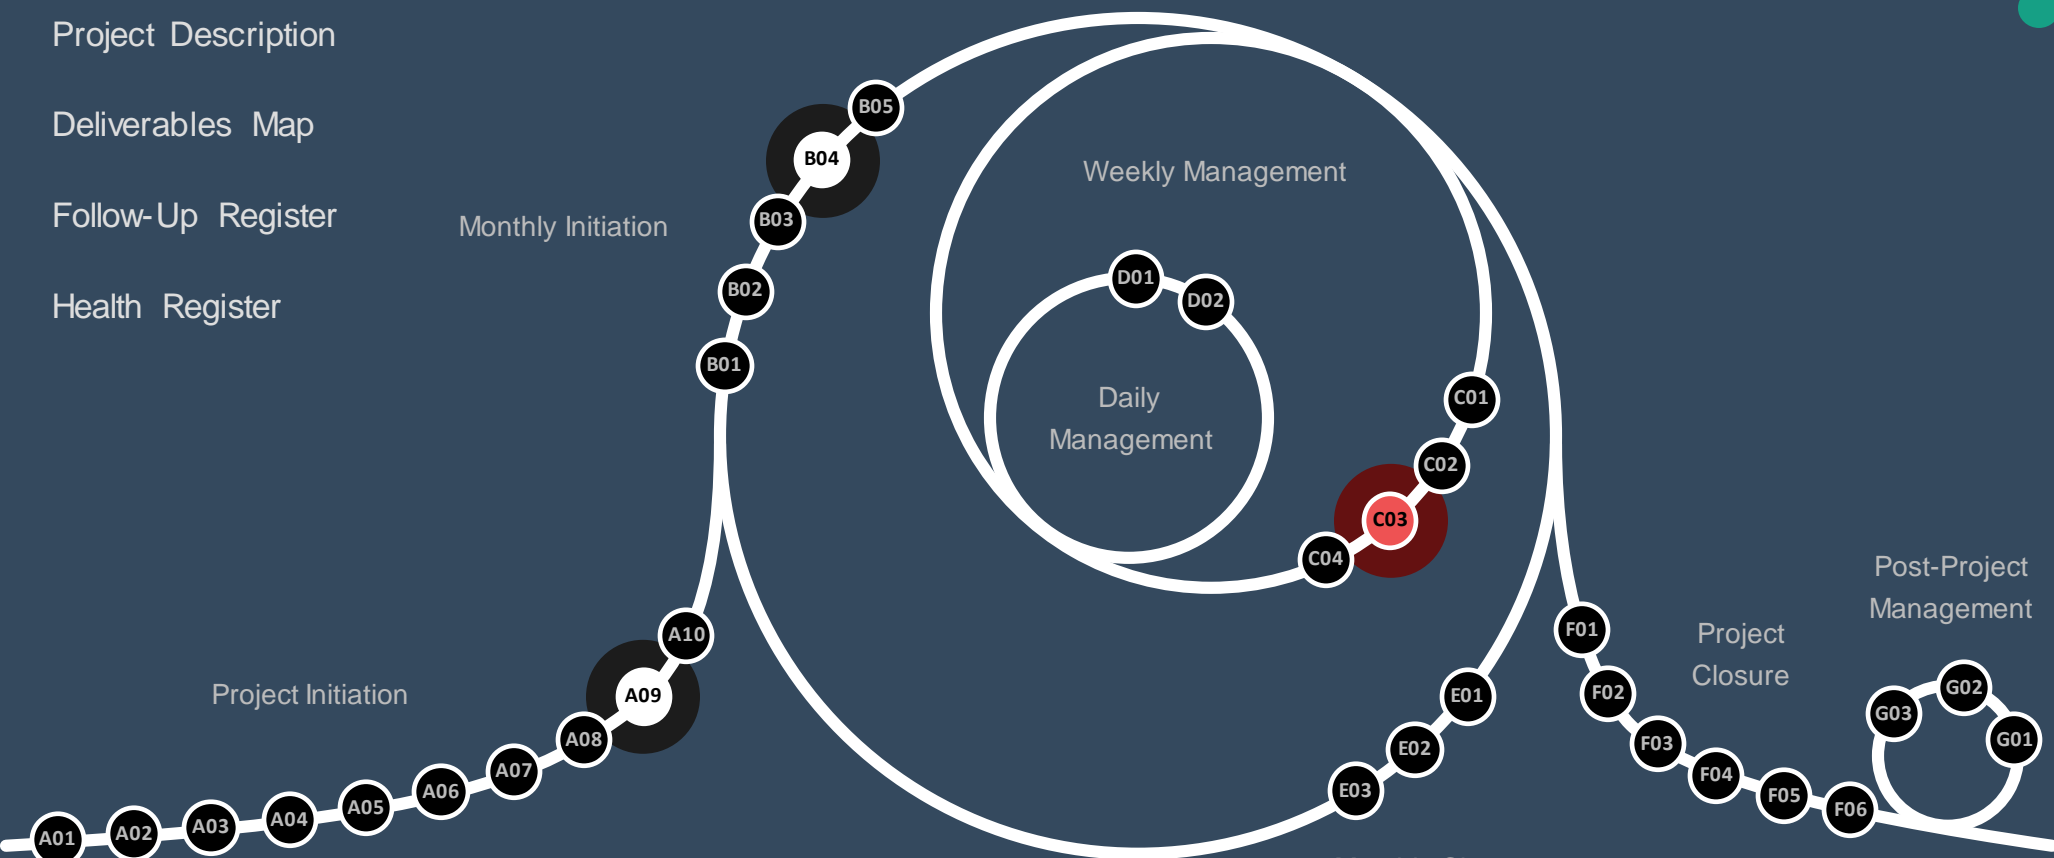

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation

Monthly Closure

Project Closure

Post-Project Management

A01

A02

A03

A04

A05

A06

A07

A08

A09

A10

B01

B02

B03

B04

B05

D01

D02

C03

C02

C01

E02

E01

F01

F02

F03

F04

F05

F06


G02

G01

G03

C04

Conduct a focused communication

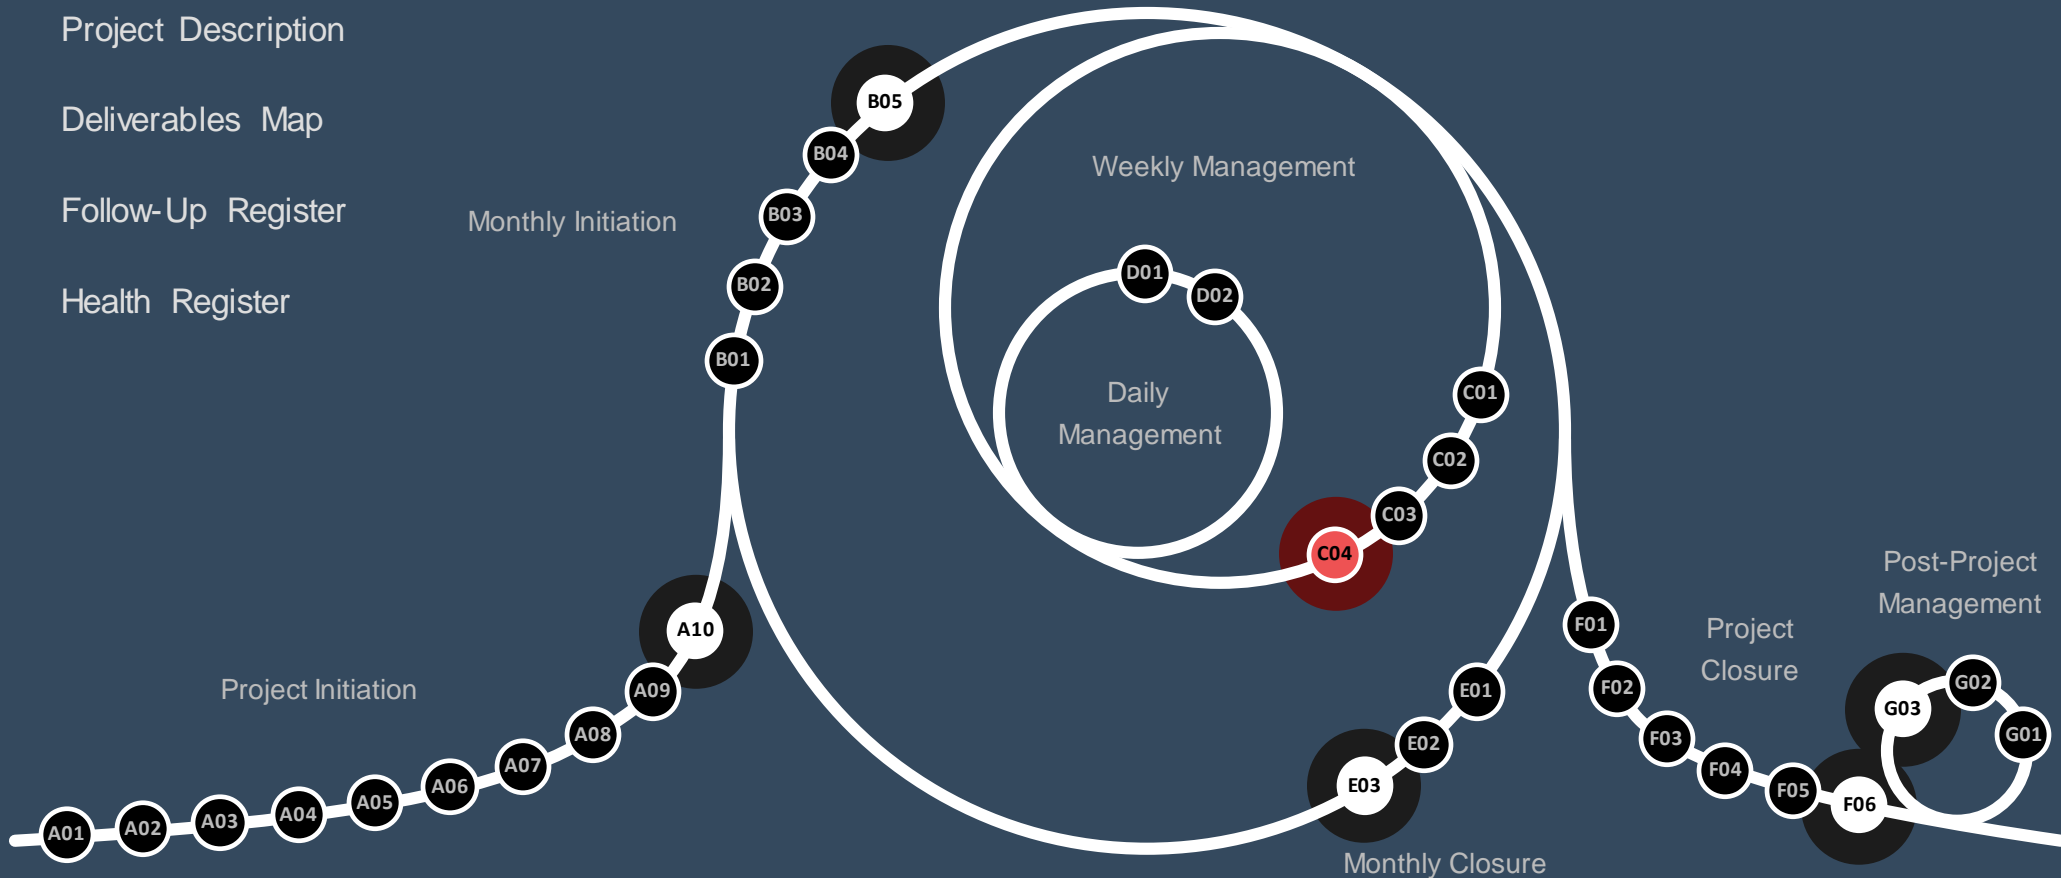

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Project Closure

Post-Project Management

Monthly Closure

D01

Manage risks, issues, and change requests

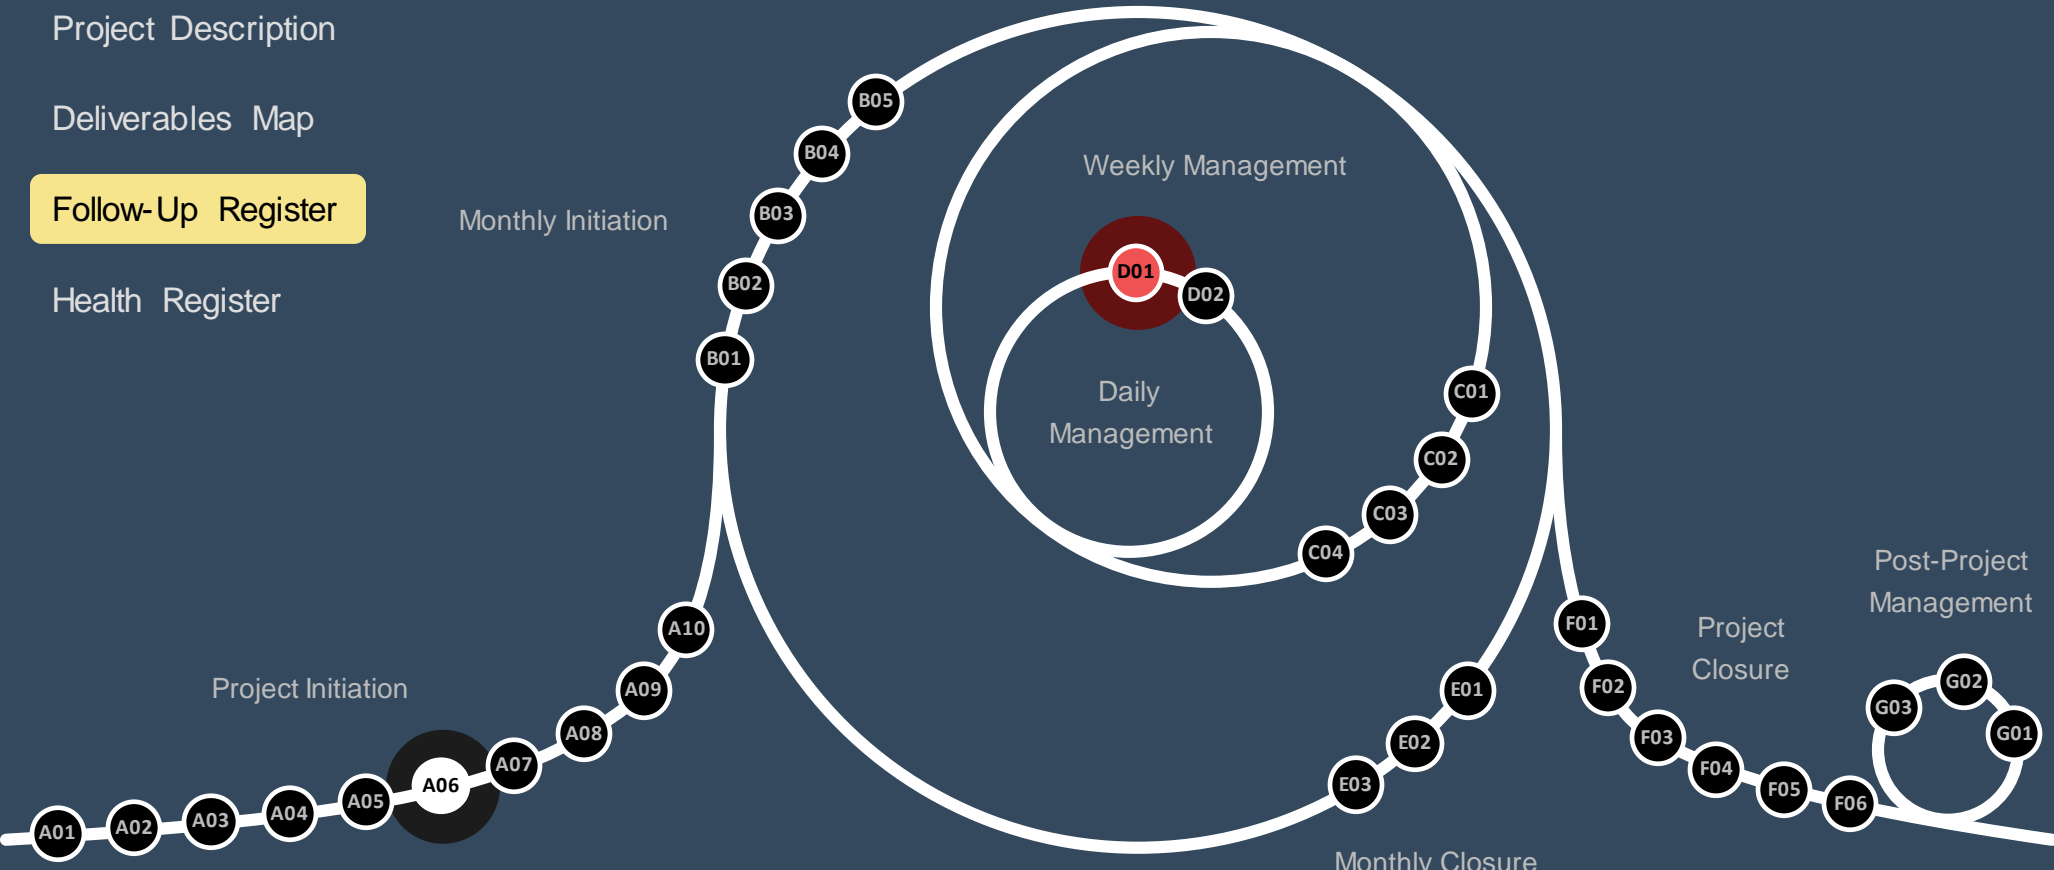

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Monthly Closure

Project Closure

Post-Project Management

D02

Accept completed deliverables

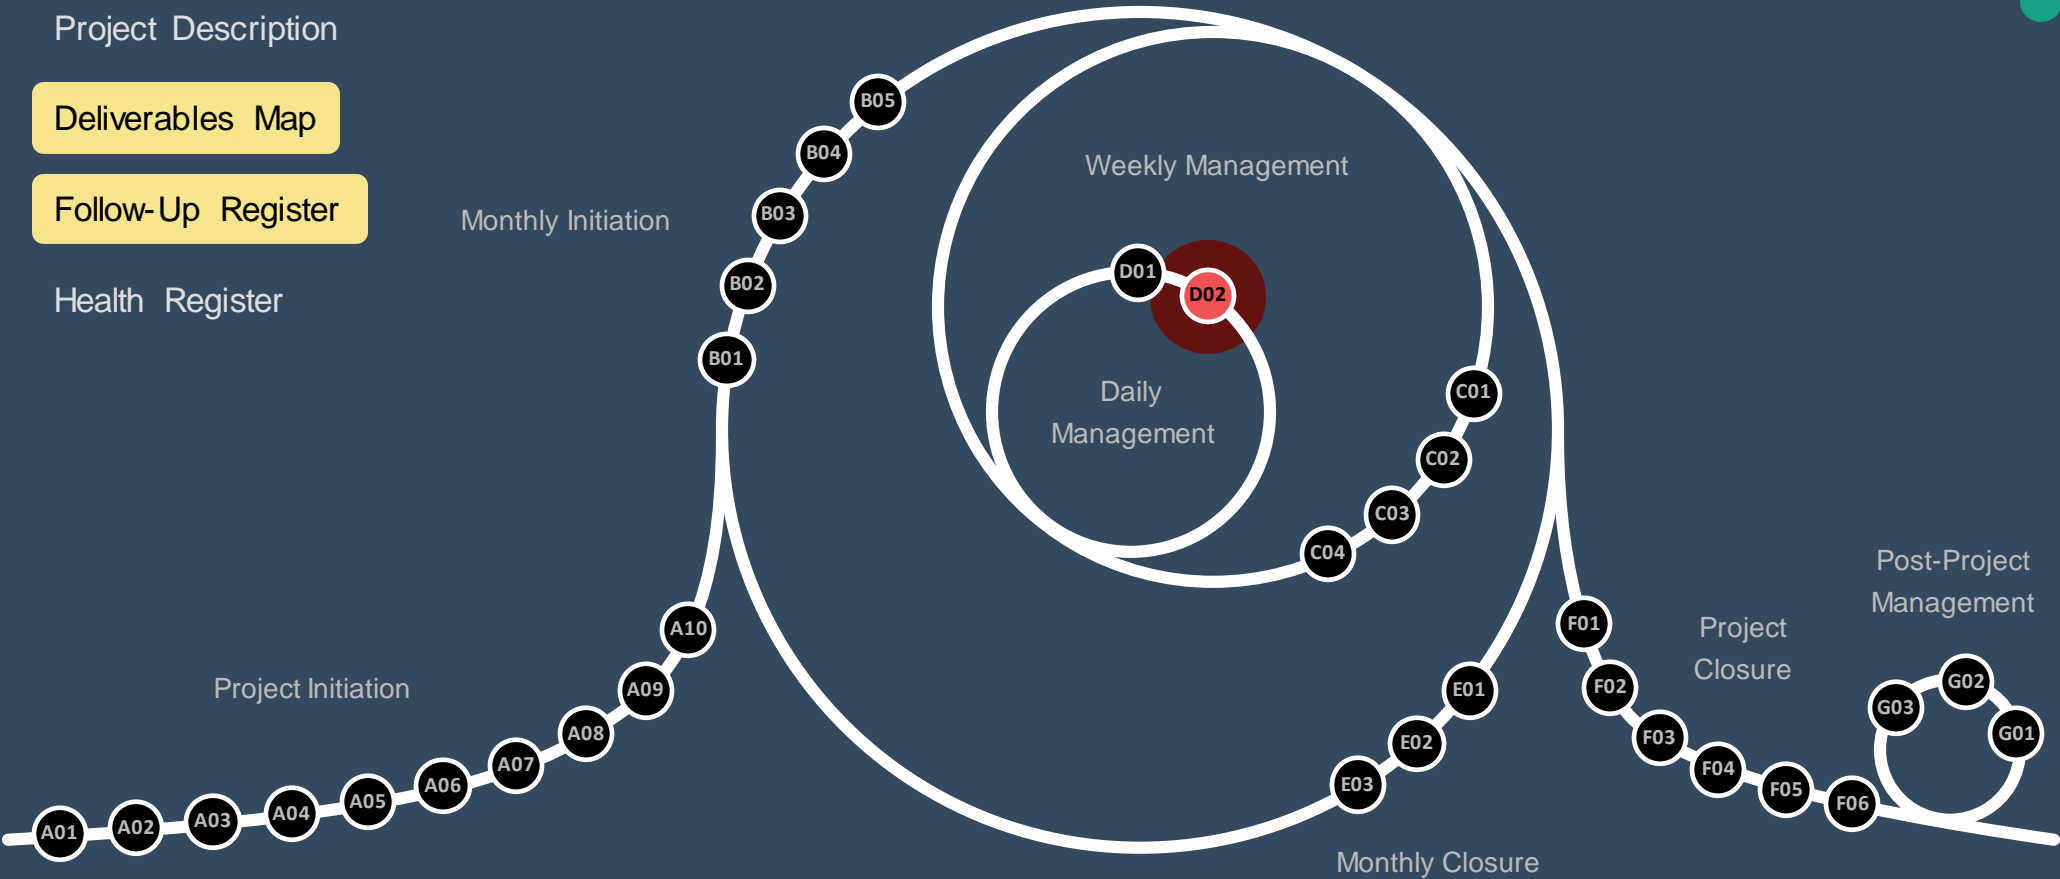


Project Description

Deliverables Map

Follow-Up Register

Health Register

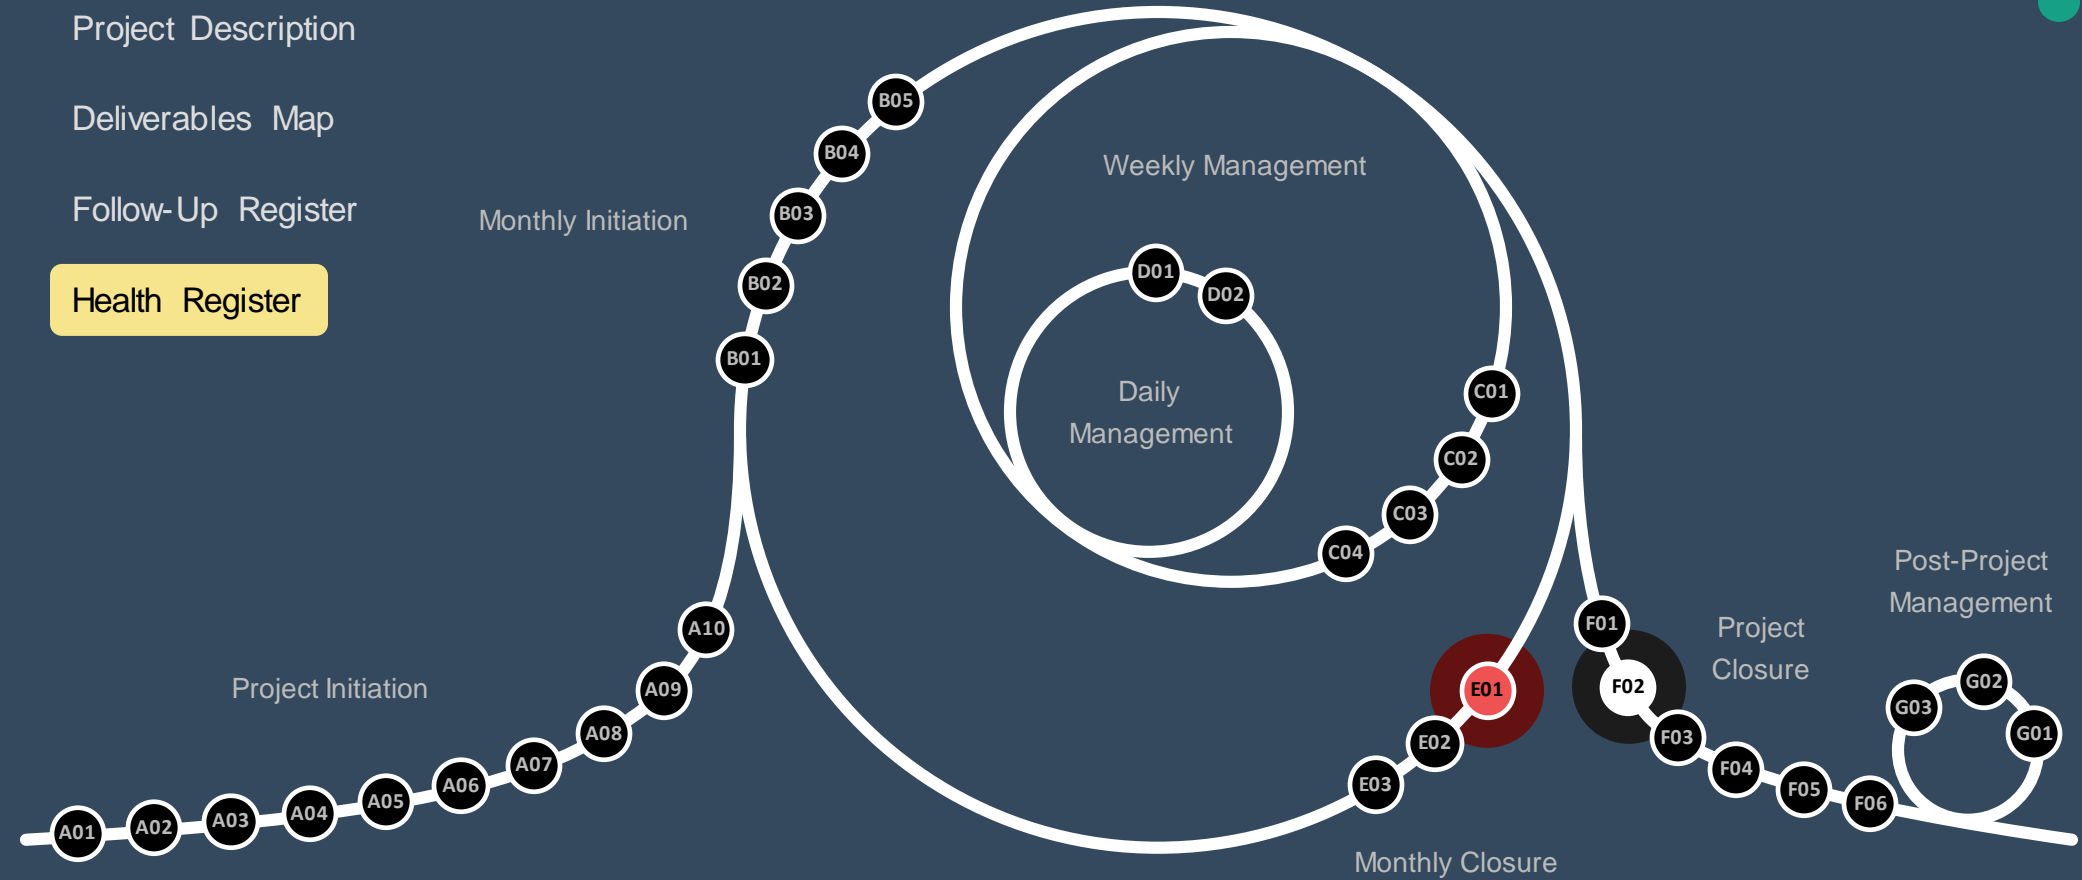

E01


Evaluate stakeholder satisfaction

Project Description

Deliverables Map

Follow-Up Register

Health Register

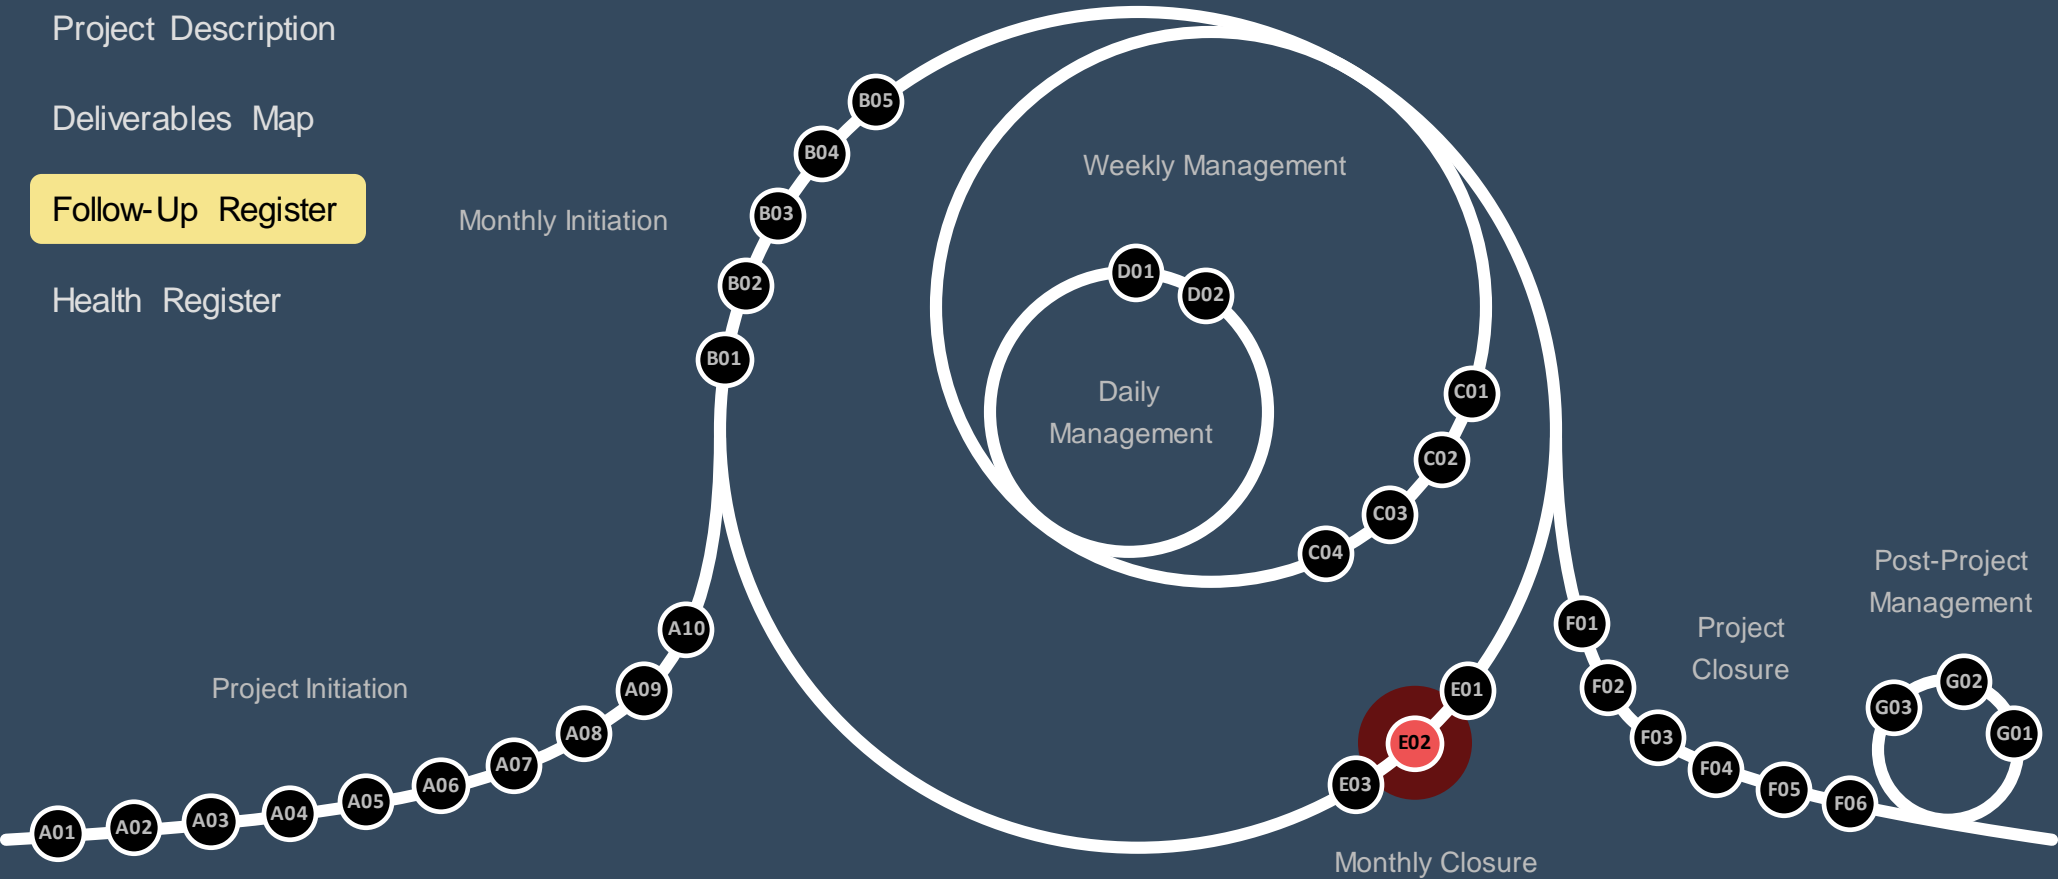

E02

Capture lessons and plan for improvements

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Project Closure

Post-Project Management

Monthly Closure

E03

Conduct a focused communication

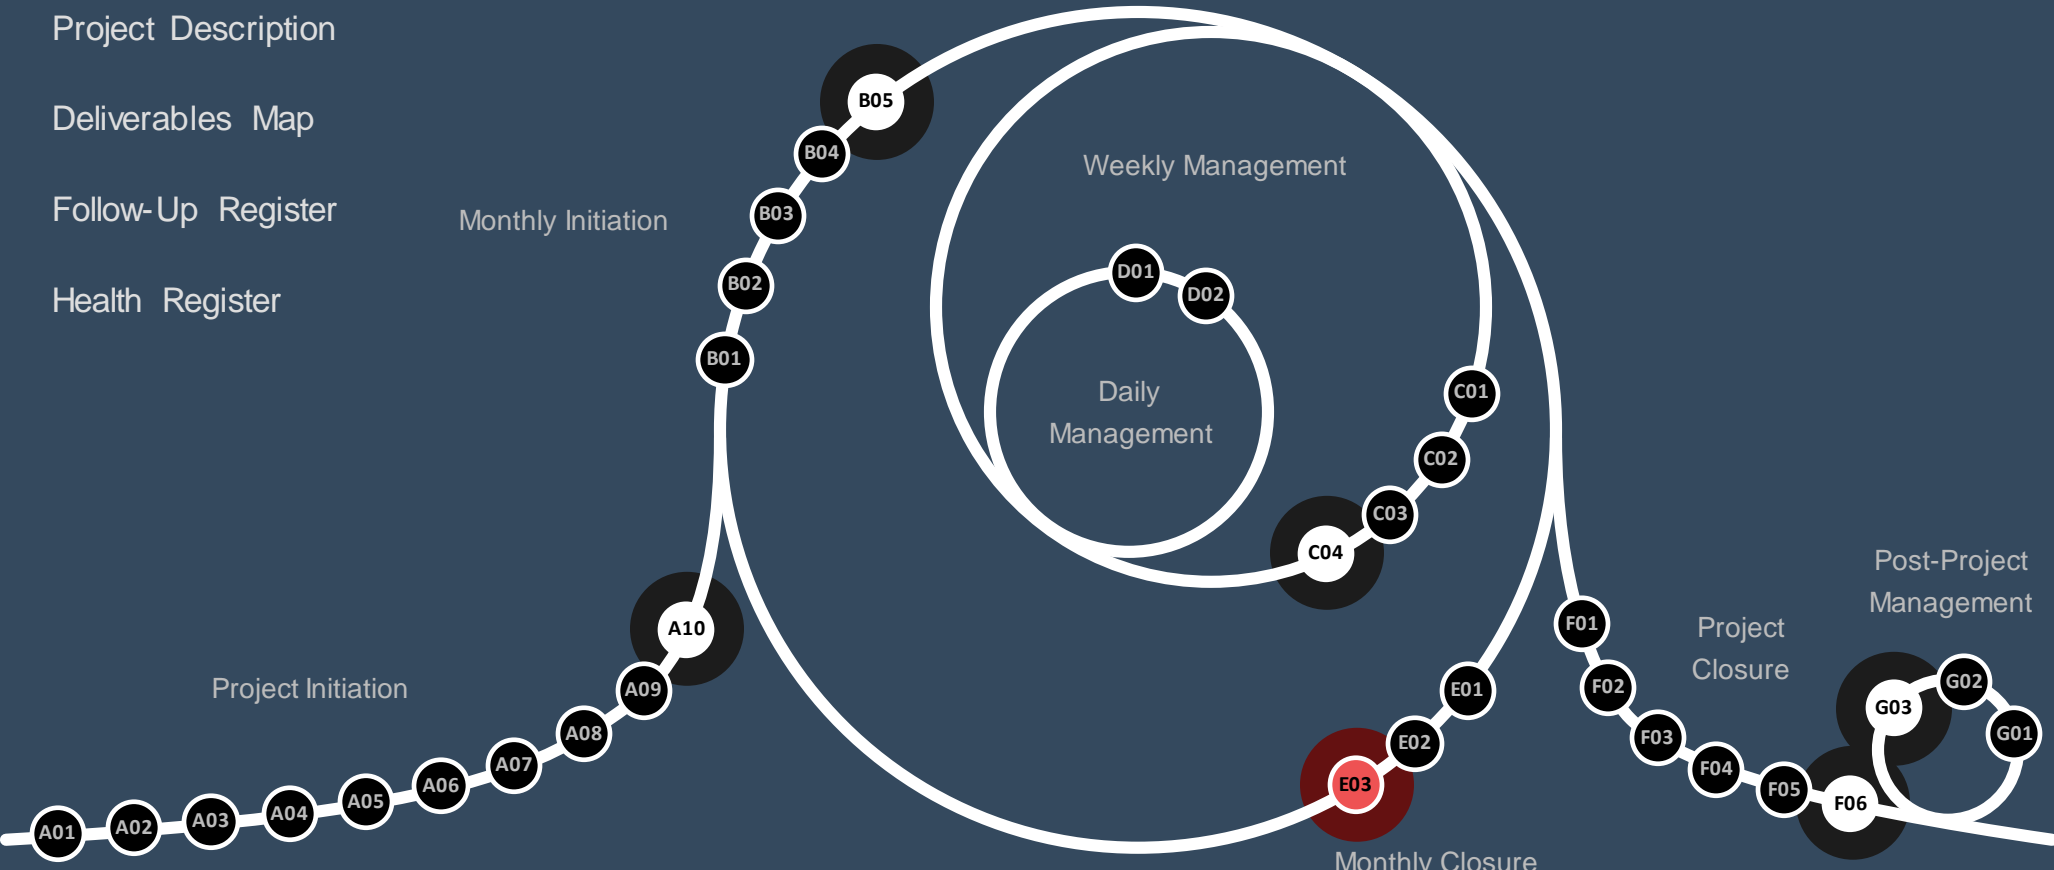


Project Description

Deliverables Map

Follow-Up Register

Health Register

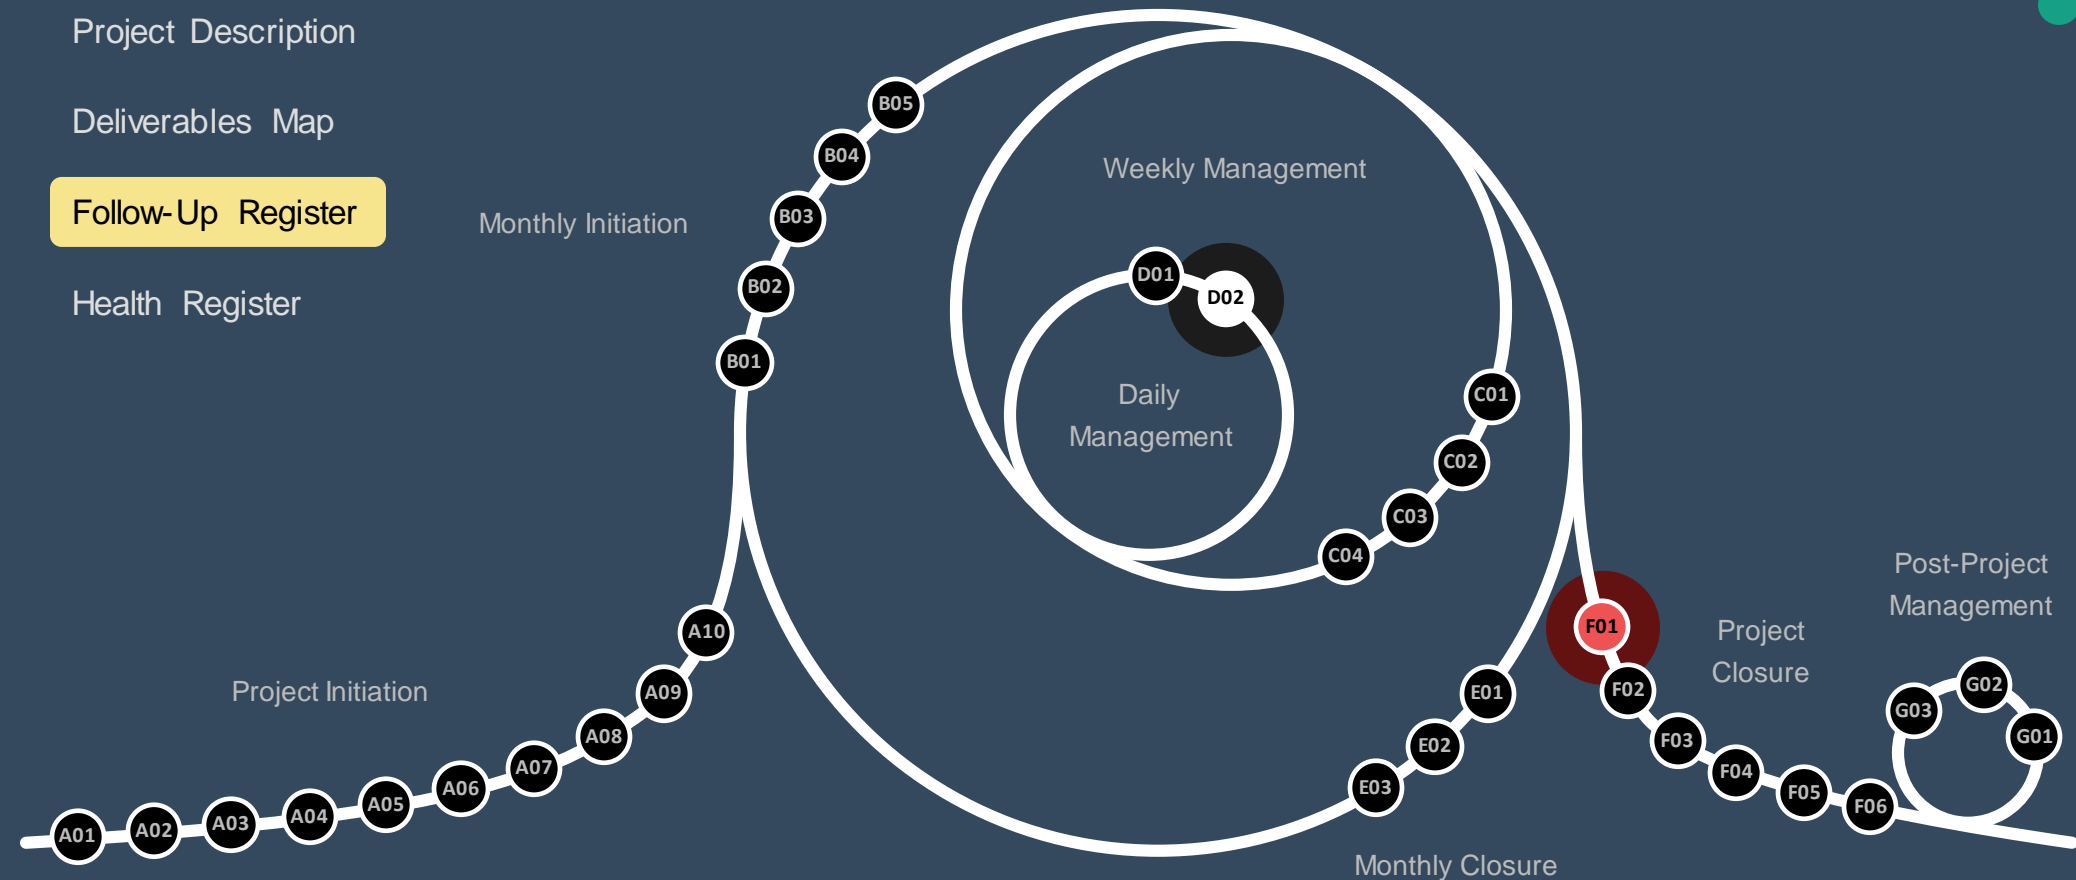

F01

Hand over the product

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Project Closure

Post-Project Management

Monthly Closure

F02

Evaluate stakeholder satisfaction

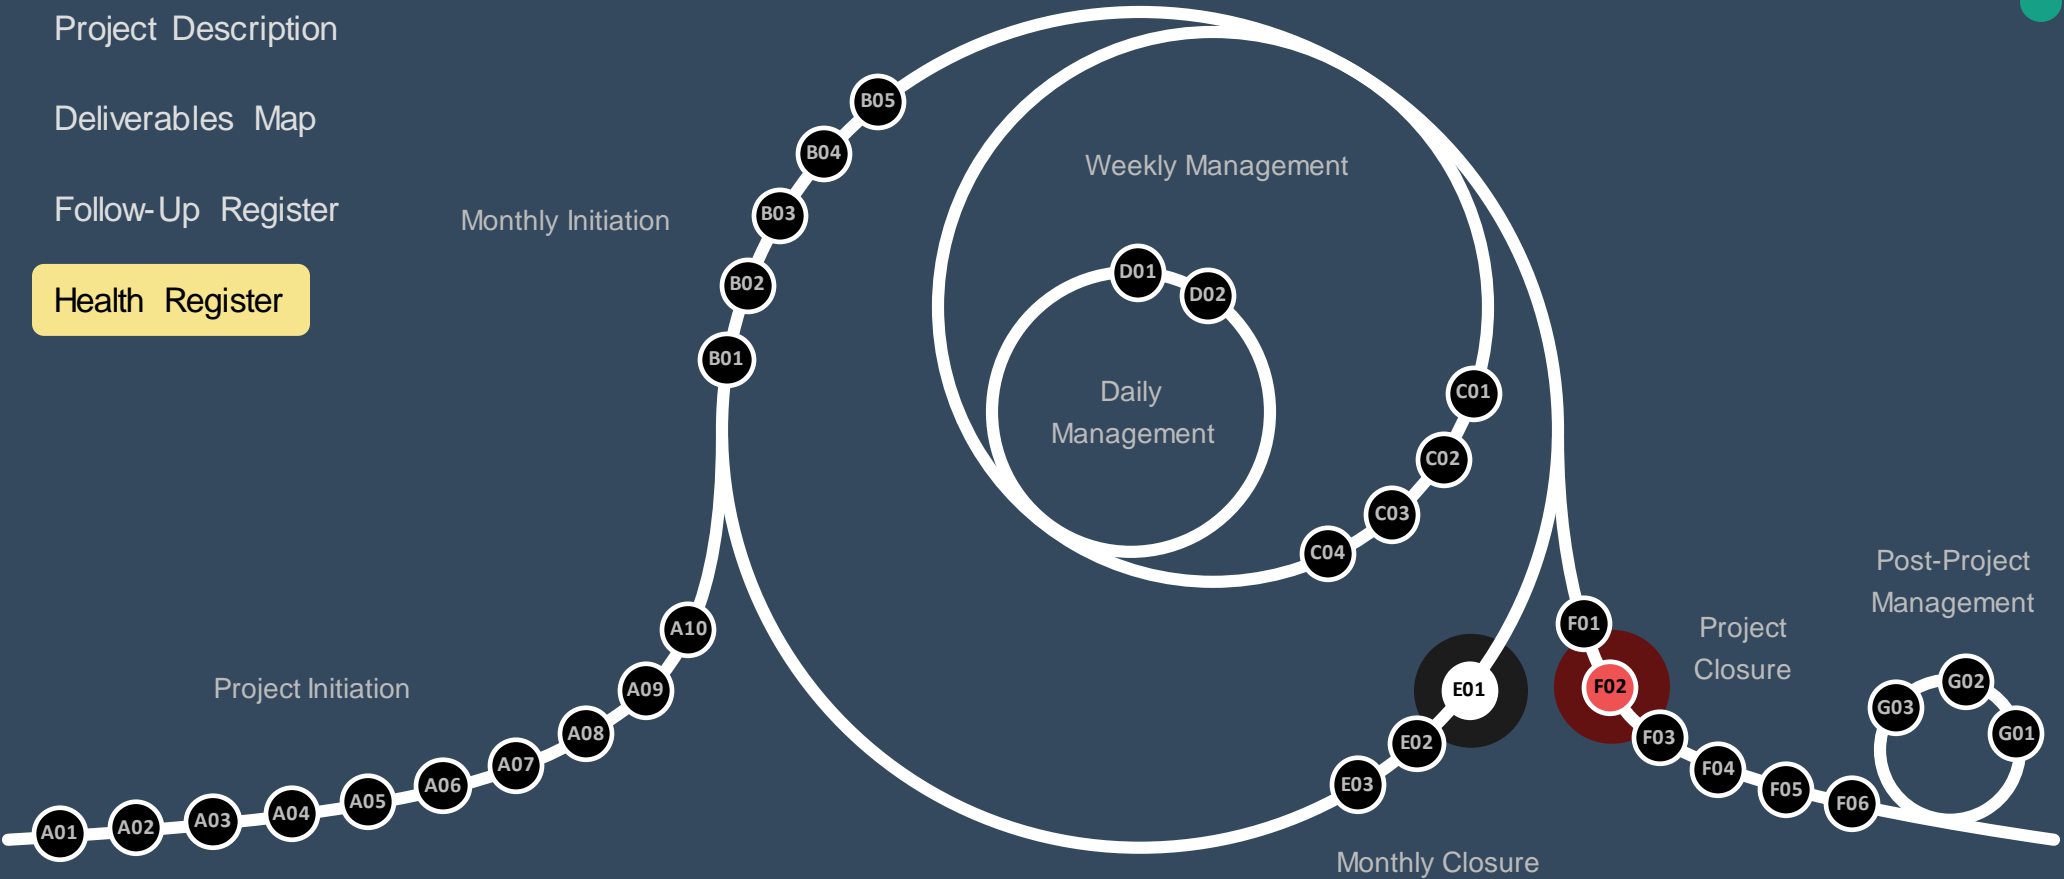

Project Description

Deliverables Map

Follow-Up Register

Health Register

Monthly Initiation

Weekly Management

Daily Management

Project Initiation


Project Closure

Post-Project Management

Monthly Closure

F03

Have the closing activity group peer-reviewed

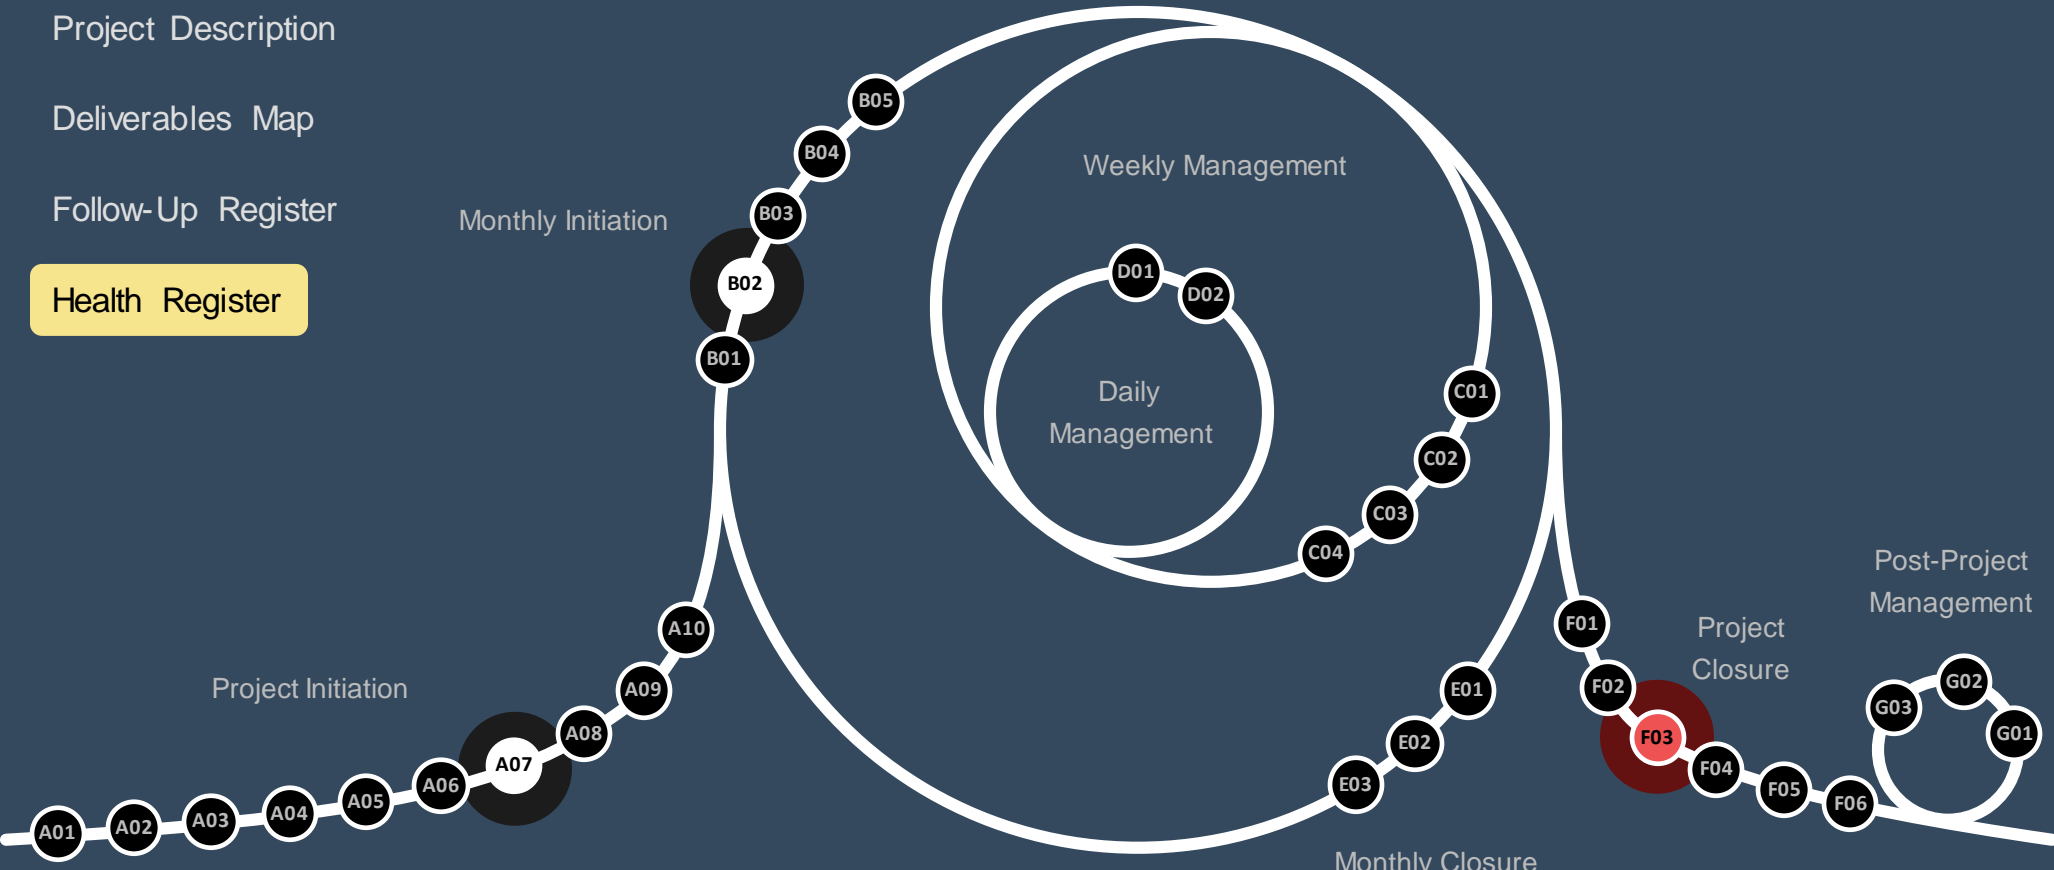


Project Description

Deliverables Map

Follow-Up Register

Health Register

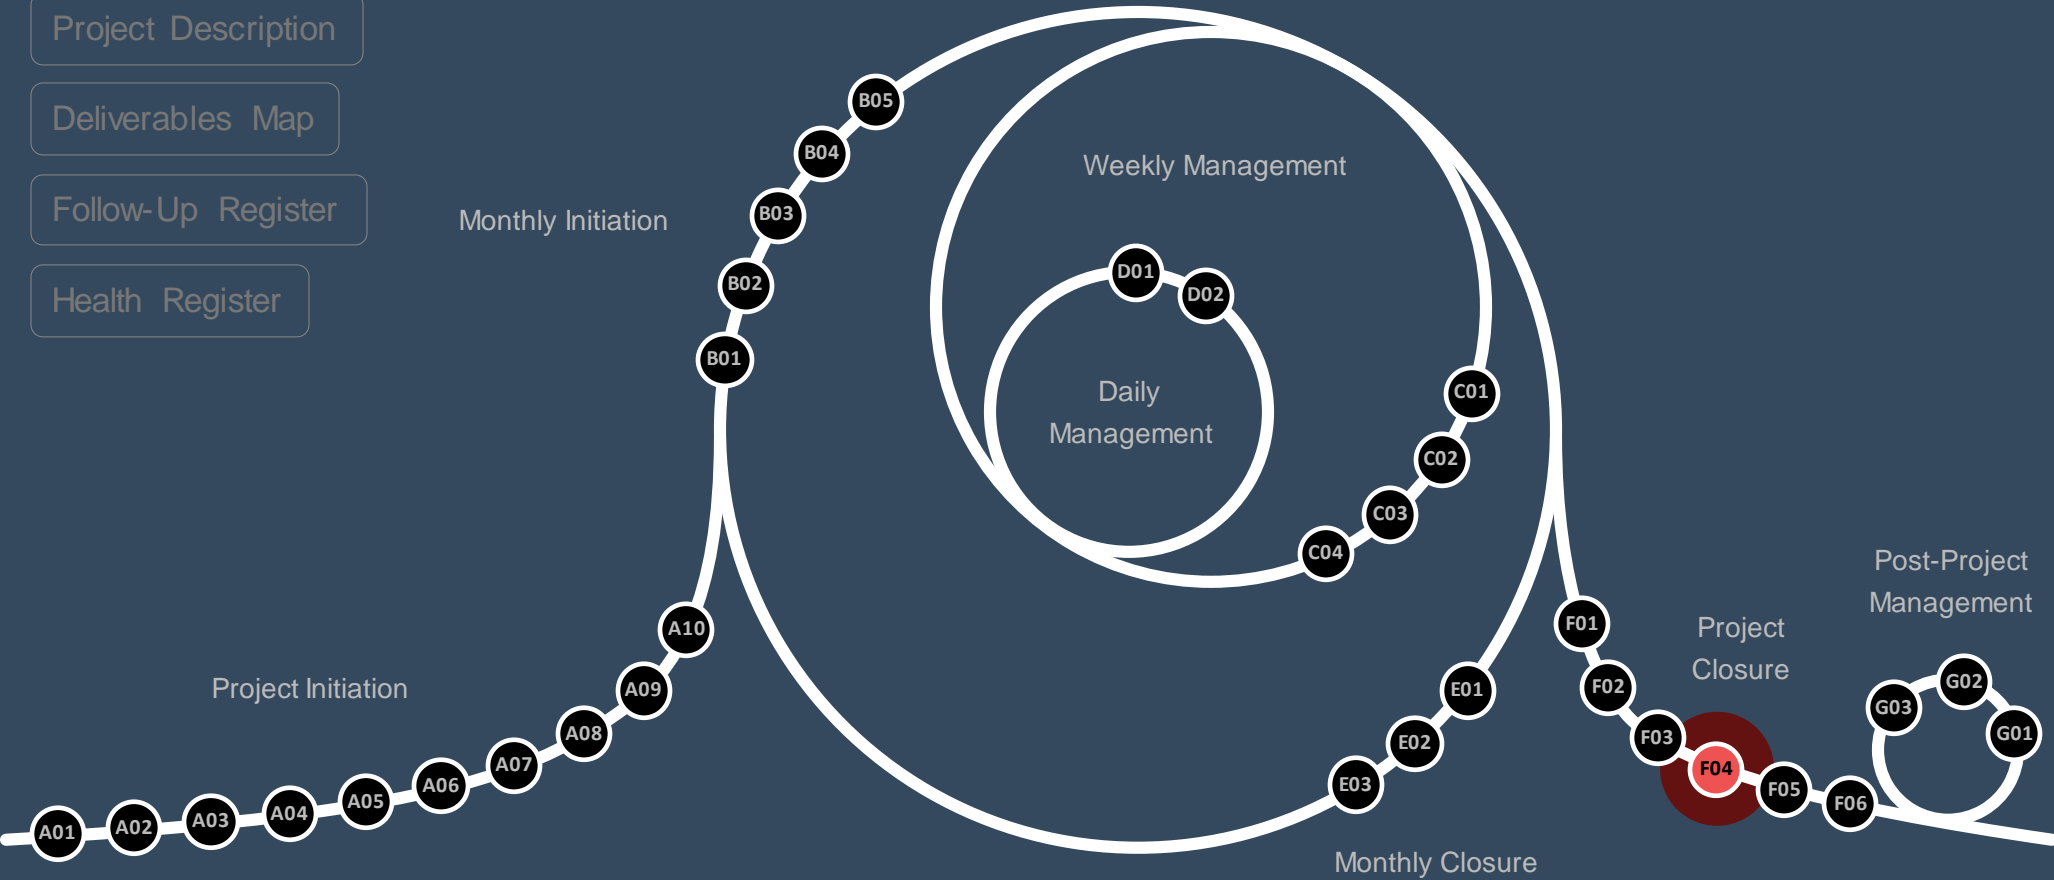

F04


Archive the project documents

Project Description

Deliverables Map

Follow-Up Register

Health Register

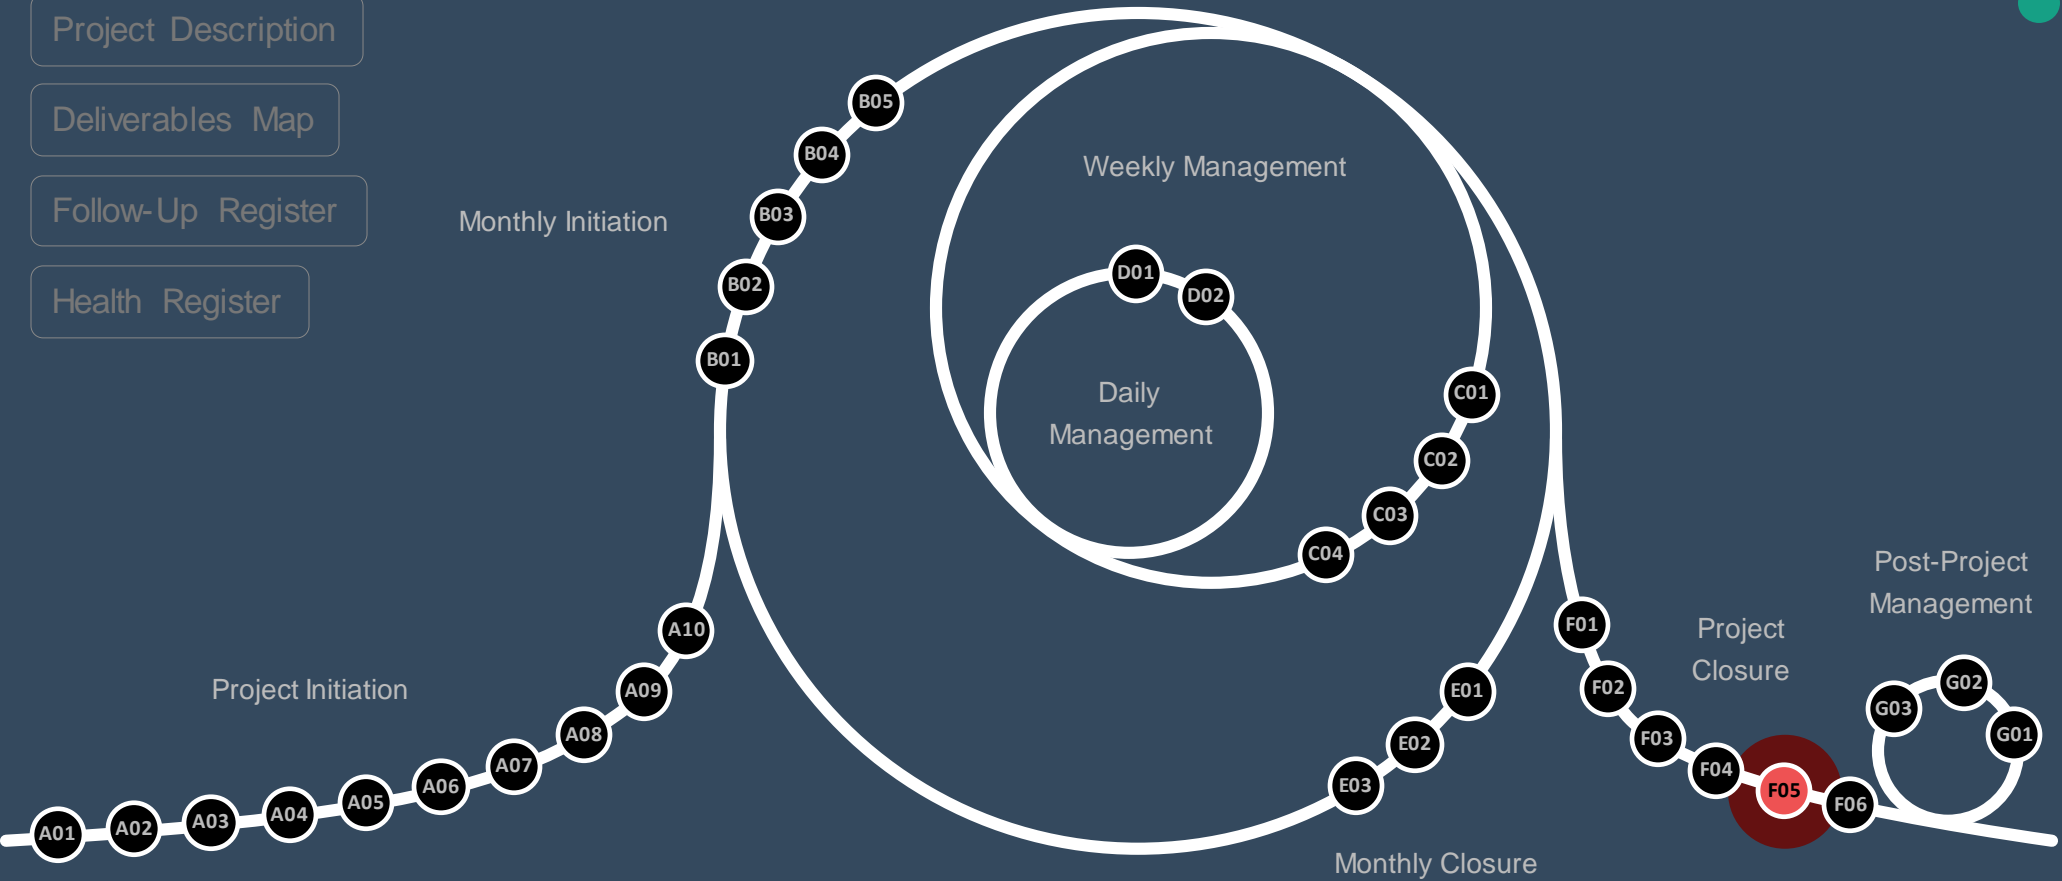

F05


Celebrate!

Project Description

Deliverables Map

Follow-Up Register

Health Register

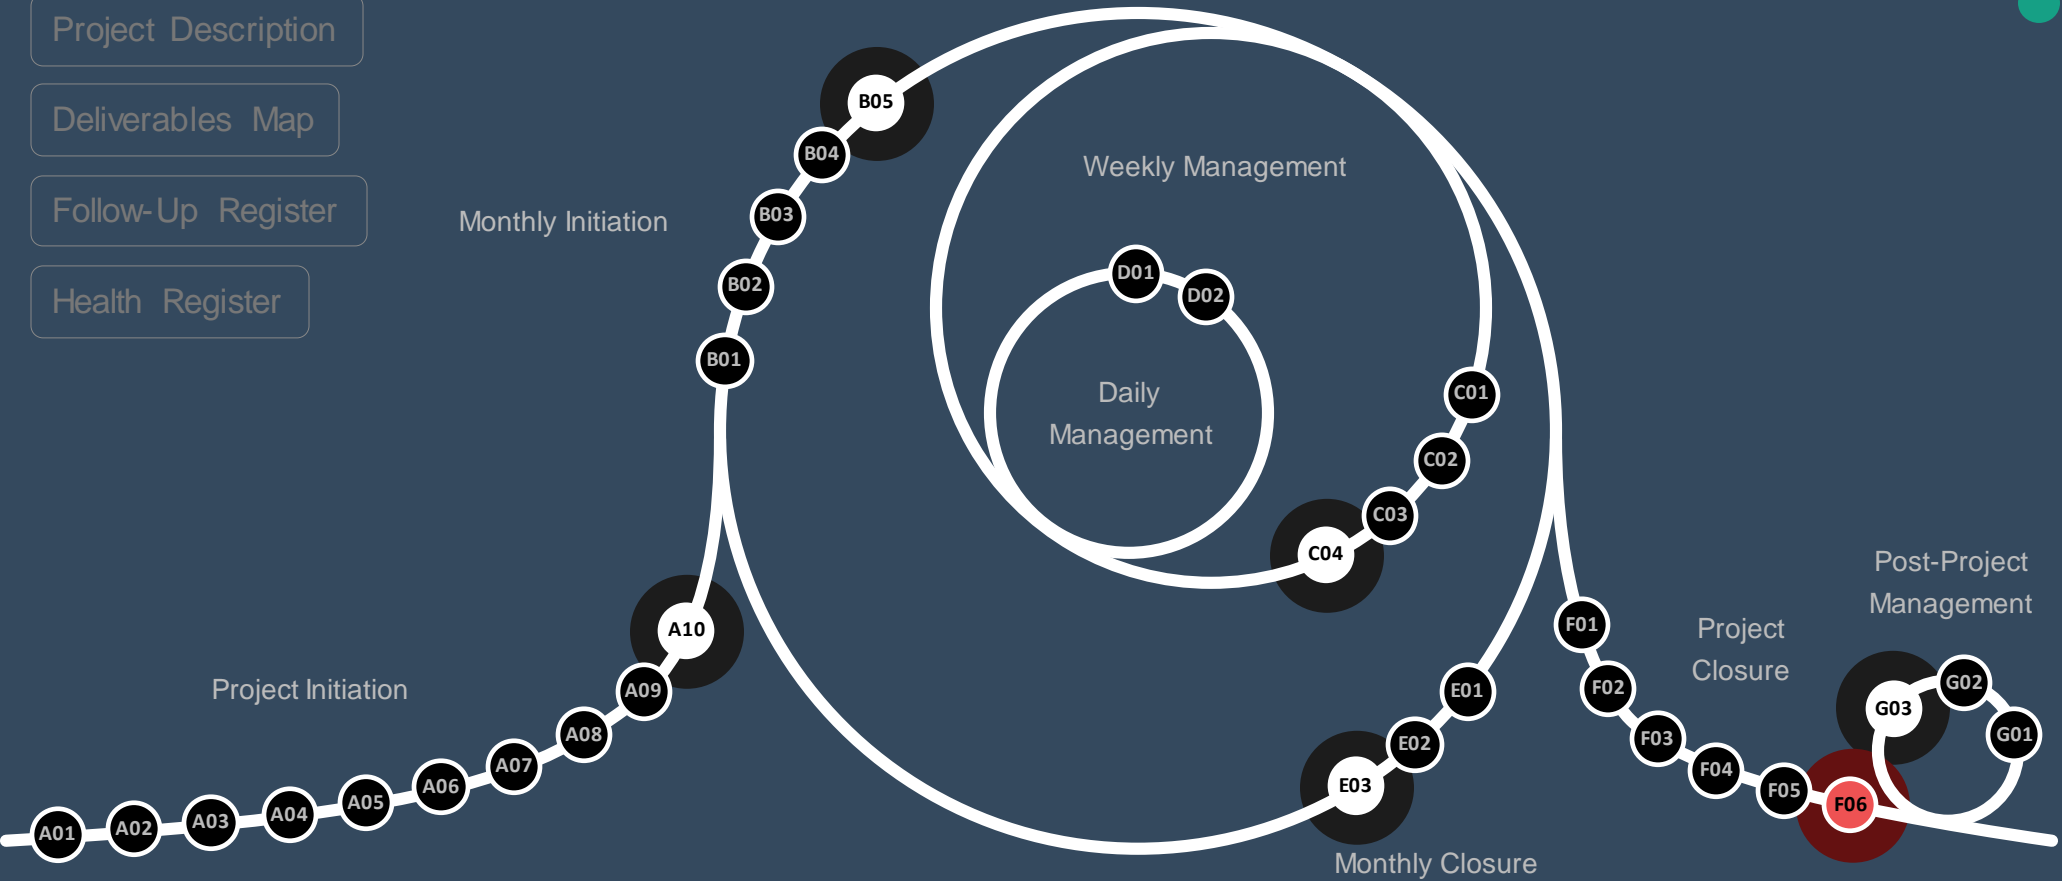

F06


Conduct a focused communication

Project Description

Deliverables Map

Follow-Up Register

Health Register

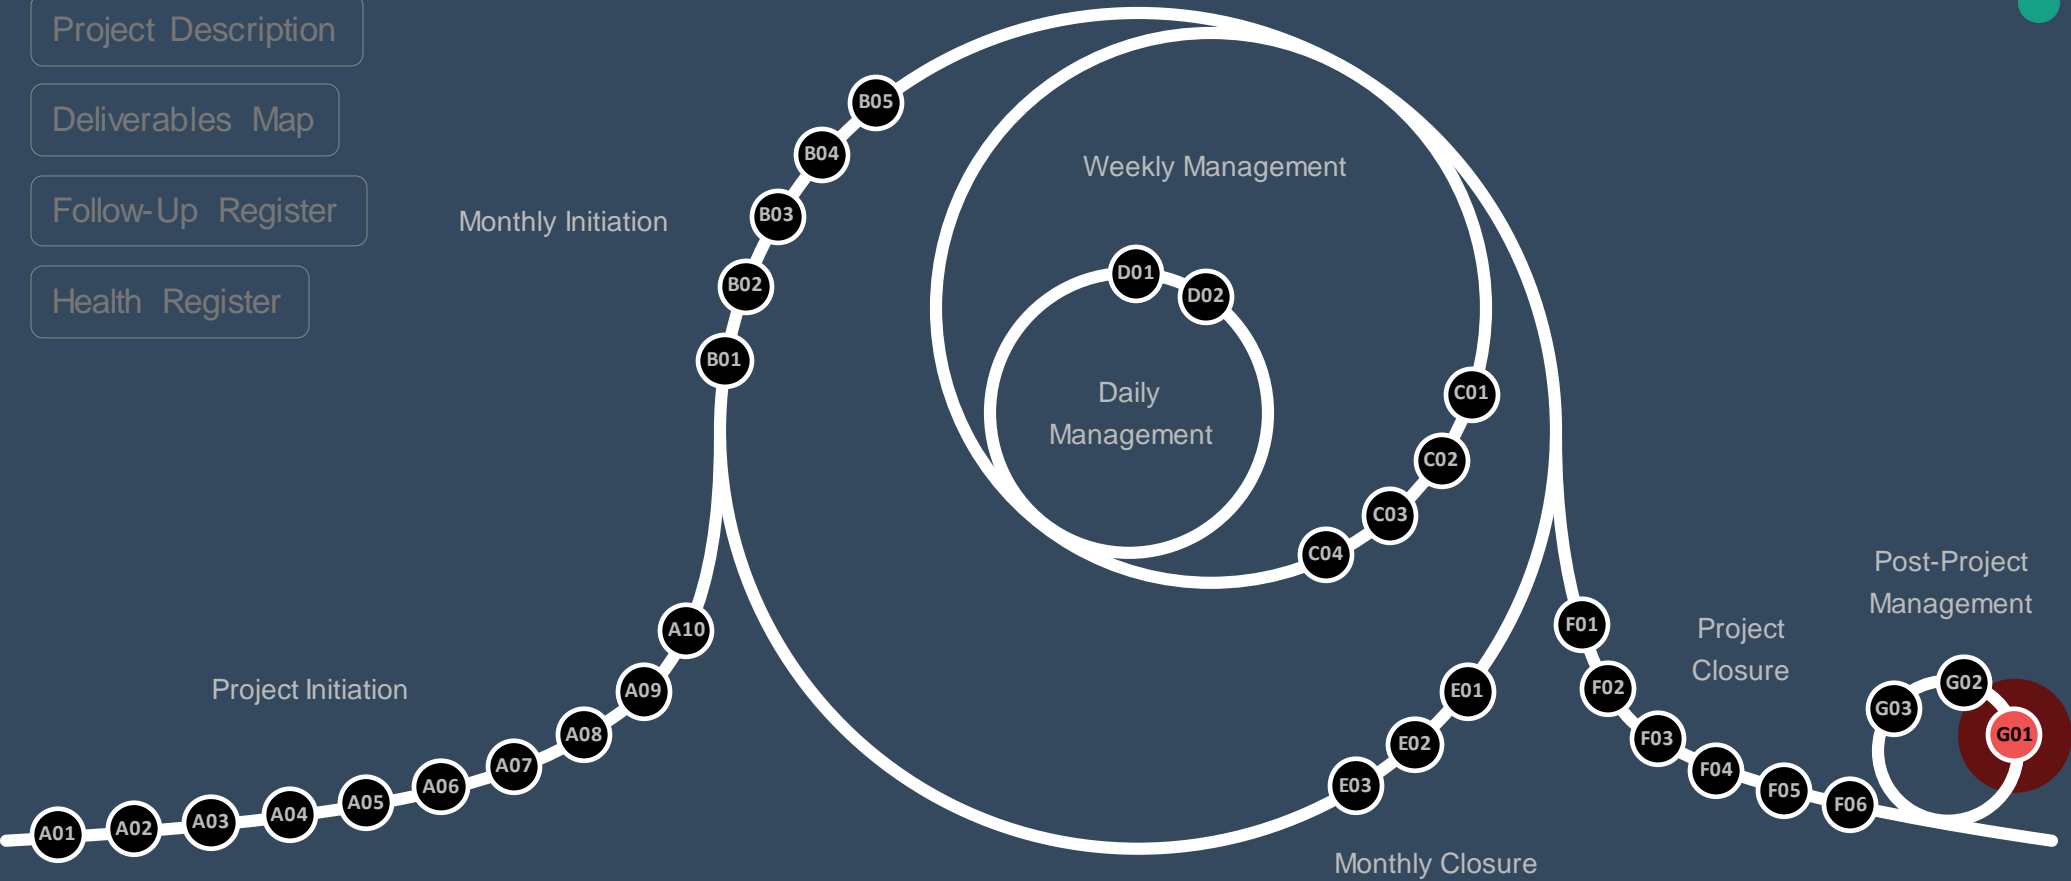

G01


Evaluate the benefits

Project Description

Deliverables Map

Follow-Up Register

Health Register

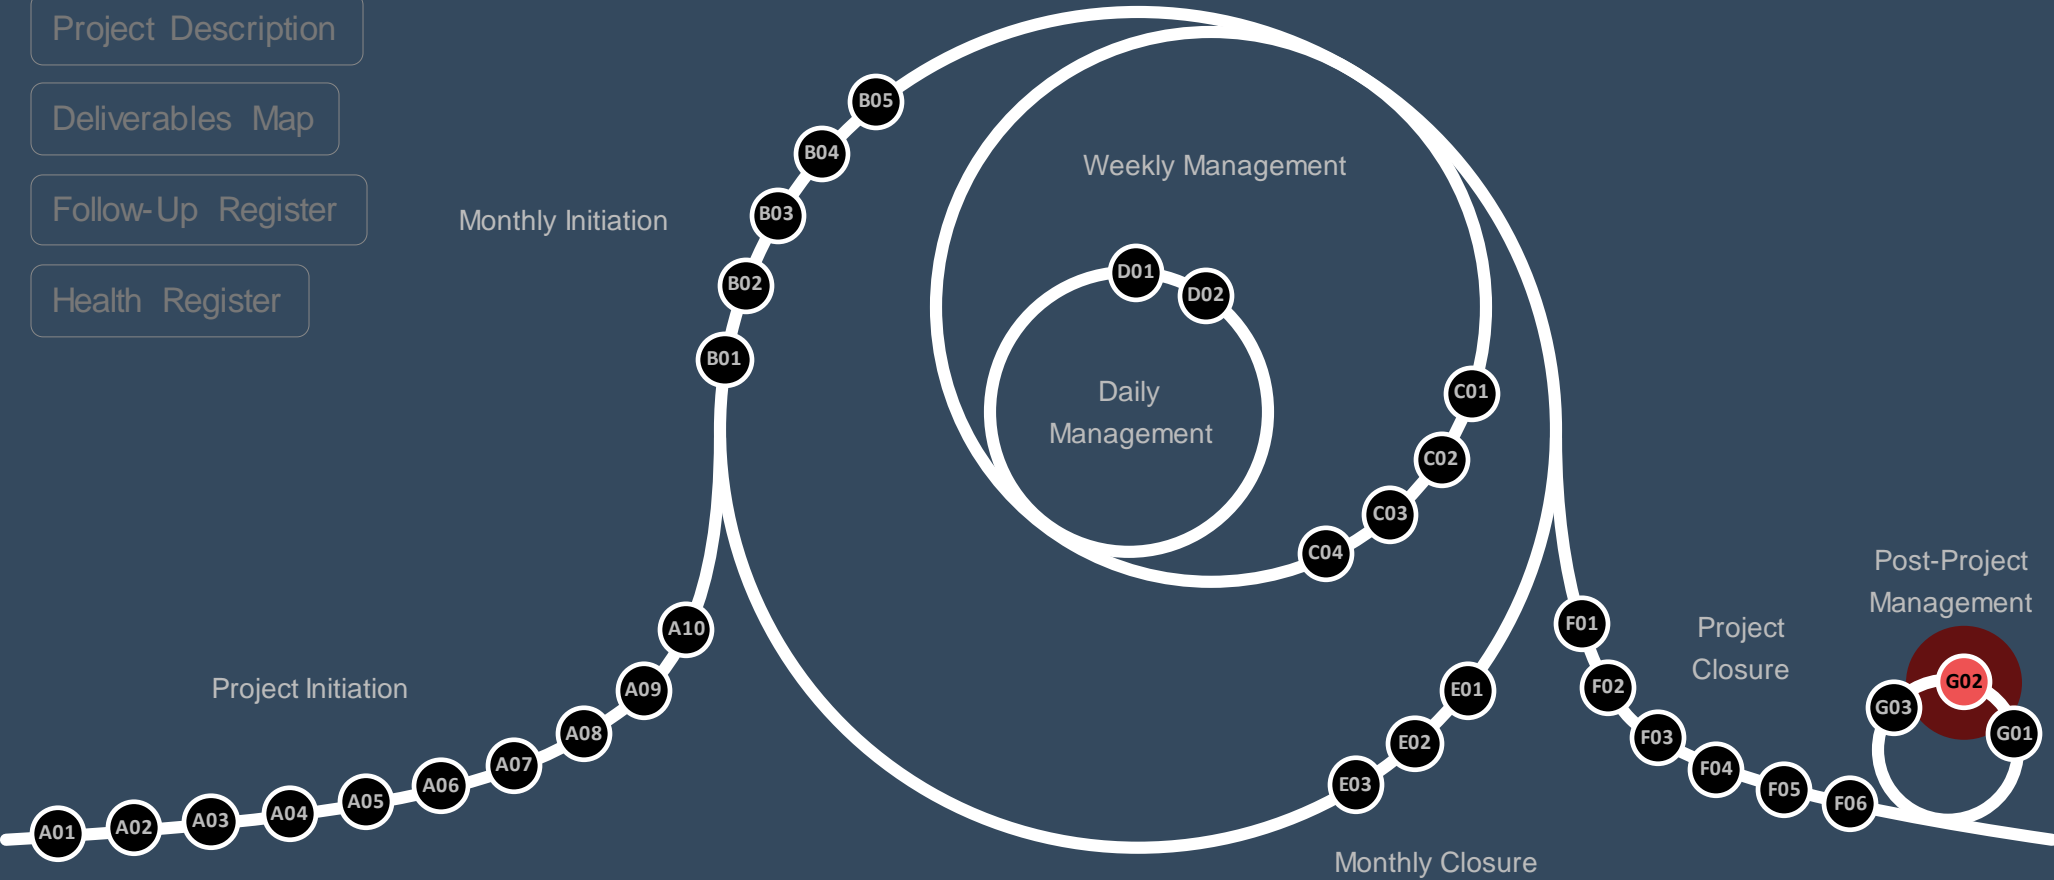

G02


Generate new ideas

Project Description

Deliverables Map


Follow-Up Register

Health Register

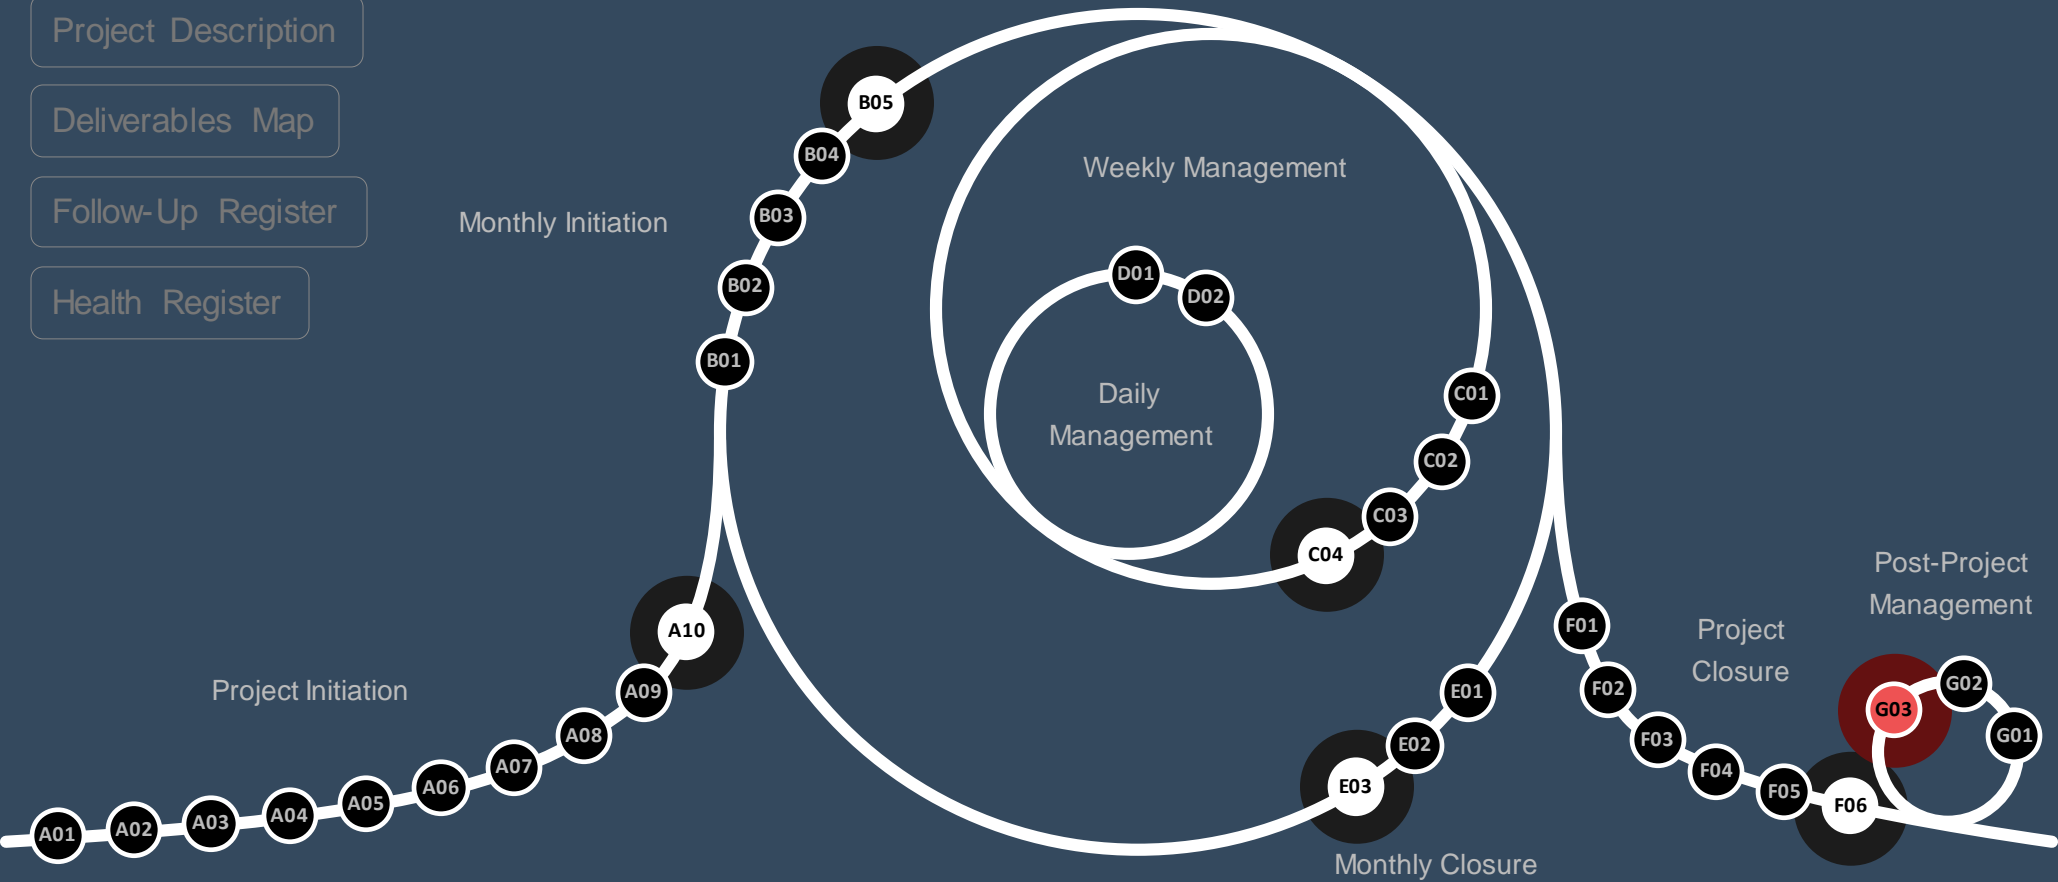

G01

Conduct a focused communication

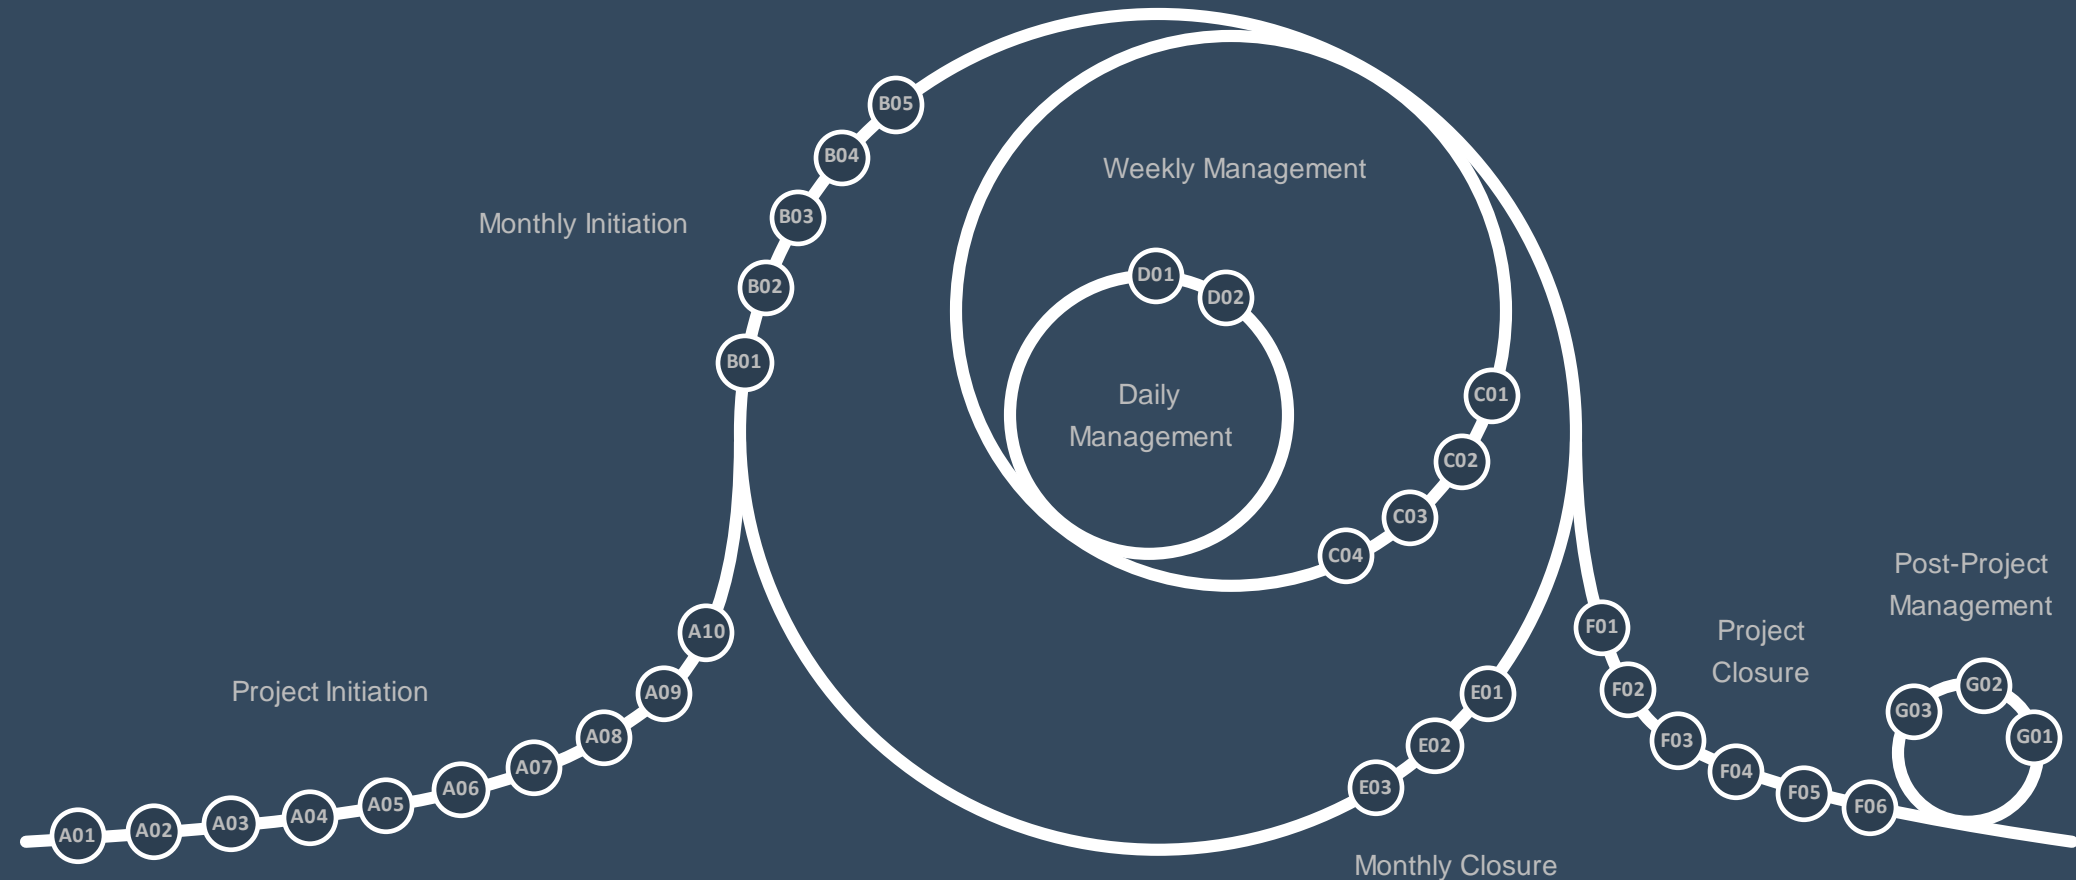

<https://p3.express/c>
